

CompTIA BrainDump JK0-017 2013-06-23

Number: 000-000
Passing Score: 800
Time Limit: 120 min
File Version: 1.0



<http://www.gratisexam.com/>

CompTIA JK0-017



CompTIA E2C Project+ Certification Exam

Version: 5.2
CompTIA JK0-017 Exam

Topic 1, Volume A

Exam A

QUESTION 1

Which of the following are process groups in the project life cycle? (Select Three).

- A. Accepting
- B. Mitigating
- C. Avoiding
- D. Initiating
- E. Closing
- F. Planning

Correct Answer: DEF

Section: (none)

Explanation

Explanation/Reference:

QUESTION 2

A project team is comfortable working as a group and has accepted all the project ground rules. They support each other to reach the project goals. Which of the following stages of team development is the project team demonstrating?

- A. Storming
- B. Performing
- C. Conforming
- D. Forming

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 3

A project manager is informed that material expenditures will increase. Which of the following documents should be referenced to address this increase?

- A. Work Breakdown Structure (WBS)
- B. Cost management plan
- C. Approved project charter
- D. Project scope document

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 4

The project charter is an output of which of the following project phases?

- A. Initiation
- B. Planning
- C. Execution
- D. Closing

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 5

All of the following are considered part of the risk management plan EXCEPT the risk:

- A. register.
- B. matrix.
- C. assessment.
- D. baseline.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 6

Which of the following is true of fast tracking a schedule?



<http://www.gratisexam.com/>

- A. Project schedule critical path will change.
- B. Project activities will be performed concurrently.
- C. Project schedule is shortened by decreasing the project scope.
- D. Project schedule lead times are increased.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 7

A project team member is uncertain how many activities are required to complete a task. Which of the following documents should be referenced?

- A. Key Performance Indicators (KPIs)

- B. Project charter
- C. Work Breakdown Structure (WBS)
- D. Statement of Work (SOW)

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 8

Which of the following is the BEST communication option for team building?

- A. Send an email transmission to introduce the project.
- B. Send a completed project charter to introduce the project.
- C. Leave a voicemail message to introduce the project.
- D. Schedule a face-to-face meeting to introduce the project.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 9

Which of the following is created using the work breakdown structure (WBS) as an input?

- A. Procurement management plan
- B. Vendor selection criteria
- C. Project scope statement
- D. Project charter

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 10

A cause and effect diagram can also be called:

- A. a control chart.
- B. a scatter diagram.
- C. an Ishikawa diagram.
- D. a Pareto Chart.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 11

In order to obtain the best pricing and product quality, a project manager should:

- A. obtain an RFP from one vendor who can provide the products.
- B. obtain an RFP from the vendor who provides the lowest priced products.
- C. obtain responses from different vendors to compare the products.
- D. use past vendors who have provided all project deliverables.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 12

A project manager has decided to increase the number of resources working on critical path activities. This is an example of:

- A. rolling wave planning.
- B. resource leveling.
- C. fast tracking.
- D. crashing.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 13

Which of the following may have a significant adverse impact upon the successful completion of an international project? (Select Three).

- A. Time zones
- B. Travel costs
- C. Co-location of resources
- D. The project plan
- E. Scheduled vacations
- F. Language barriers

Correct Answer: ABF

Section: (none)

Explanation

Explanation/Reference:

QUESTION 14

A project manager is presented with a change request for an ongoing project. Which of the following would be the FIRST action?

- A. Update the project plan to accommodate the changes.

- B. Perform an impact analysis.
- C. Organize a stakeholder meeting to review the changes.
- D. Change the project scope to reflect the change request.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 15

Which of the following are created using information contained in the work breakdown structure (WBS)? (Select Two).

- A. Project scope statement
- B. Project statement of work
- C. Project charter
- D. Project activity estimates
- E. Project resource estimates

Correct Answer: DE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 16

Which of the following steps should a project manager take to ensure the quality of project deliverables for a customer? (Select Two).

- A. The project manager should consult the project sponsor and customer to review the current quality requirements.
- B. The project manager should request a peer review of the project to determine if it meets the customers quality standards.
- C. The project manager should change the scope of the project to meet the customers expectations of quality standards.
- D. The project manager should check the finished product to determine if it meets the customers quality standards.
- E. The project manager should outsource to obtain the best resources for the project.

Correct Answer: BD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 17

A product has been sent to an outside vendor for testing. During their testing it was determined that the product is not meeting the quality standards. The project manager scheduled a meeting to review their findings. Which of the following BEST describes this situation?

- A. Quality assurance

- B. Quality control
- C. Quality analysis
- D. Quality planning

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 18

The project manager crashes a project that is behind schedule and under-budget. Which of the following will be the intended result?

- A. The project will be behind schedule and over-budget.
- B. The project will be on schedule but over-budget.
- C. The project will be on schedule and on-budget.
- D. The project will be behind schedule and on-budget.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 19

Which of the following methods would a project manager use to estimate the construction cost of a 2,000 square foot home when given the cost per square foot?

- A. Parametric estimating
- B. Analogous estimating
- C. Top-down estimating
- D. Bottom-up estimating

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 20

A project manager is performing activity sequencing using the arrow diagramming method (ADM). Which of the following is true of ADM?

- A. ADM can only represent finish to start dependencies.
- B. ADM cannot represent multiple successor activities.
- C. ADM can only represent activities that are on the critical path.
- D. ADM uses boxes representing activities, and arrows to represent dependencies.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 21

Which of the following represents the appropriate order of an effective change management process?

- A. Identify change, perform impact analysis, approve or deny change, update applicable project plan components, document change.
- B. Identify change, document change, perform impact analysis, approve or deny change, update applicable project plan components.
- C. Identify change, document change, perform impact analysis, update applicable project plan components, approve or deny change.
- D. Identify change, document change, approve or deny change, perform impact analysis, update applicable project plan components.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 22

Which of the following conflict resolution techniques is used to get people to face their conflicts directly and work through the issues?

- A. Confronting
- B. Forcing
- C. Compromising
- D. Smoothing

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 23

In which of the following organization types would a project manager have the MOST authority?

- A. Projectized
- B. Balanced Matrix
- C. Weak Matrix
- D. Functional

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 24

Which of the following would be a direct output of the initiating process group? (Select Two).

- A. Project charter
- B. Project management plan
- C. Statement of Work (SOW)
- D. Work Breakdown Structure (WBS)
- E. Preliminary scope statement

Correct Answer: AE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 25

Which of the following cost estimating techniques uses previous, similar projects as a basis of estimating costs for the current project?

- A. Top-down estimating
- B. Parametric estimating
- C. Bottom-up estimating
- D. Analogous estimating

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 26

Which of the following tools are used for quality planning? (Select Two).

- A. Cost / Benefit analysis
- B. Network diagram
- C. Benchmarking
- D. Critical Path Method (CPM)
- E. Parametric estimating

Correct Answer: AC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 27

Which of the following is a use for a Pareto diagram?

- A. In procurement management to evaluate vendor proposals.
- B. In cost management to determine actual versus expected project costs.
- C. In quality management to identify and prioritize problem areas.
- D. In risk management to assess potential project risk occurrences.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 28

Which of the following quality control tools illustrates the various factors that may be linked to potential problems or effects?

- A. Ishikawa diagram
- B. Histogram
- C. Run chart
- D. Scatter diagram

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 29

Which of the following risk response strategies involves shifting the negative impact of a threat, along with ownership of the response, to a third party?

- A. Risk transfer
- B. Risk avoidance
- C. Risk sharing
- D. Risk mitigation

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 30

Which of the following risk response strategies involves the use of insurance, performance bonds, or warranties?

- A. Risk acceptance
- B. Risk mitigation
- C. Risk avoidance
- D. Risk transfer

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 31

During which of the following process groups is the preliminary project risk assessment performed?

- A. Monitoring/Controlling
- B. Planning
- C. Initiating
- D. Executing

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 32

During which of the following process groups is the availability of required resources for the project determined?

- A. Executing
- B. Monitoring/Controlling
- C. Initiating
- D. Planning

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 33

Which of the following describes the point in time when resources can be assigned to scheduled tasks?

- A. When the project statement of work (SOW) has been created
- B. When the project deliverables have been defined
- C. When the work breakdown structure (WBS) is decomposed into work packages
- D. When the project WBS dictionary has been created

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 34

In which of the following organization types is it LEAST likely that a conflict regarding competing demands for resources would take place?

- A. Functional
- B. Weak Matrix
- C. Balanced Matrix
- D. Projectized

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 35

Which of the following elements does a project charter contain?

- A. A project scope statement
- B. A change management template
- C. A completed request for proposal (RFP)
- D. A complete list of the key performance indicators (KPIs)

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 36

A project can be defined as which of the following?

- A. A high level cost estimate
- B. An ongoing work assignment
- C. A temporary endeavor with unlimited time or cost for completion
- D. A temporary endeavor limited by time or cost

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 37

Which of the following elements would be needed to prepare an effective project scope document?

- A. An approved project milestone schedule
- B. An approved risk assessment document
- C. An approved project charter
- D. A responsibility assignment matrix

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 38

Which of the following should be created in the project closing documentation? (Select Two).

- A. Closure report summarizing costs
- B. Responsibility assessment matrix

- C. Lessons learned
- D. Project timeline
- E. Statement of Work (SOW)

Correct Answer: AC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 39

Given the circumstances below, which of the following would be the BEST action for the project manager to take?

1. One of the key stakeholders disagrees with the project.
 2. Two of the key staff members refuse to work with each other.
 3. The budget for the project has been reduced.
 4. The scope of the project has changed.
-
- A. The staff members who refuse to work together should be terminated so that the project can proceed on schedule.
 - B. The project should be closed because the scope has changed.
 - C. The project manager should work with the stakeholders to resolve the areas of disagreement.
 - D. The project manager should fast track the schedule because the project budget was reduced.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 40

Two of the stakeholders cannot agree on the project timeline or budget. The project is critical to the success of the company. Which of the following actions should the project manager take NEXT?

- A. Invite all of the stakeholders to a meeting to discuss project requirements.
- B. Document the points of agreement and create the timeline and budget based upon the expectations of the majority of the stakeholders.
- C. Modify the project scope to bring it into alignment with the stakeholders expectations.
- D. Inform the stakeholders that the project will be cancelled if they cannot agree.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 41

Several managers are sharing a project team member, which is impacting the progress of both projects. Which of the following BEST describes the situation?

- A. Varying work styles
- B. Schedule variance
- C. Scope creep
- D. Competing resource demands

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 42

Which of the following occurs during a project kick-off meeting? (Select Two).

- A. Work performance information is established.
- B. Risk analysis is performed.
- C. Quality metrics are defined.
- D. Project goals are communicated.
- E. Roles and responsibilities of the project team are identified.

Correct Answer: DE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 43

A project manager has failed to obtain the necessary permits from the local building commission. The project has been stopped because of a failure to understand the importance of:

- A. internal process compliance.
- B. risk avoidance.
- C. standards compliance.
- D. audit trail compliance.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 44

A project budget has been reduced by 10 percent, but the project has a critical deadline. Which of the following should the project manager do FIRST to complete the project on time?

- A. Lower the quality standards for the finished product.
- B. Analyze the impact of the change.
- C. Eliminate 10 percent of the projects resources.
- D. Document the approved change request.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 45

Key resources on a project are being shared. The stakeholders are aware of the shared resources and do not expect this to impact the progress of the project. In which of the following should the shared resource be documented?

- A. Quality management metrics
- B. Work Breakdown Schedule (WBS)
- C. Scope statement
- D. Risk register

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 46

Several key resources will be unavailable at the end of the project. The key stakeholders want to outsource the project to a third party. Which of the following risk responses is described in this situation?

- A. Risk avoidance
- B. Risk mitigation
- C. Risk acceptance
- D. Risk transference

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 47

A customer requests that the products quality be reduced to control its cost. Which of the following actions should the project manager take FIRST?

- A. Modify the project schedule.
- B. Obtain approval for the change.
- C. Reduce the amount of project resources to control costs.
- D. Modify the project budget.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 48

Which of the following components are included in a communication plan? (Select Two).

- A. Statement of Work (SOW)
- B. Risk matrix
- C. Frequency



<http://www.gratisexam.com/>

- D. Work Breakdown Structure (WBS)
- E. Distribution list

Correct Answer: CE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 49

Which of the following documents is used when soliciting vendors?

- A. Request for Proposal (RFP)
- B. Work Breakdown Structure (WBS)
- C. Statement of Work (SOW)
- D. Responsibility Assignment Matrix (RAM)

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 50

Which of the following components is included in a transition plan?

- A. Ownership
- B. Quality metrics
- C. Project budget
- D. Quality baseline

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 51

All of the following occur during the project closure phase EXCEPT:

- A. ensure the project is aligned with organizational goals.
- B. ensure document retention compliance is being performed.
- C. release project team resources.
- D. close contracts and pay vendors.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 52

Which of the following actions would require a formal project closure? (Select Two).

- A. The project is delayed indefinitely because a required vendor part cannot be delivered.
- B. The project is producing a product that is no longer compliant with new Federal regulations.
- C. The project work is completed.
- D. The project has run out of money.
- E. The project sponsor has become disinterested in the project.

Correct Answer: CD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 53

The lessons-learned activity and formal acceptance documentation form part of which of the following process groups?

- A. Closing
- B. Planning
- C. Executing
- D. Monitoring/Controlling

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 54

The purpose of a WBS dictionary is to provide:

- A. additional details for each component of the WBS, and for each component provide a brief definition of its statement of work, outputs, actual activities and pertinent milestones.
- B. a detailed glossary of terms used in the WBS.
- C. written authorization to sanction work on a particular work-package within the WBS, and define the methods for its implementation and the monitoring of its performance.
- D. a hierarchical decomposition of the work to be undertaken to address the objectives and meet the requirements of the project at the lowest level.

Correct Answer: A
Section: (none)
Explanation

Explanation/Reference:

QUESTION 55

Which of the following would measure a project's validity?

- A. Risk analysis
- B. Strategic alignment
- C. Resource allocation
- D. Gantt chart

Correct Answer: B
Section: (none)
Explanation

Explanation/Reference:

QUESTION 56

The project team is recognized for contribution efforts and is officially released from the project during which of the following stages?

- A. Formal acceptance
- B. Administrative closure
- C. Lessons learned
- D. Transition plan

Correct Answer: B
Section: (none)
Explanation

Explanation/Reference:

QUESTION 57

A project manager has a project with staff in four different countries. When generating the resource management plan, which of the following should be considered FIRST?

- A. Reviewing holiday and vacation schedule with all team members.
- B. Getting the email address of all the employees.
- C. Locating each employee on the map in the office.
- D. Understanding the international country code of all the team members.

Correct Answer: A
Section: (none)
Explanation

Explanation/Reference:

QUESTION 58

Which of the following quality option costs BEST identifies the expense of inspecting deliverables to prevent flawed products from reaching the customer?

- A. Actual costs
- B. Failure costs
- C. Appraisal costs
- D. Contract costs

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 59

A project manager receives formal leadership authority from which of the following documents?

- A. Resource matrix
- B. Project charter
- C. Work Breakdown Structure (WBS)
- D. Statement of Work (SOW)

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 60

Which of the following would be goals of an effective kick-off meeting? (Select Two).

- A. To create the project charter
- B. To create the statement of work (SOW)
- C. To outline the communication plan
- D. To set team member expectations
- E. To determine the critical path of the project

Correct Answer: CD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 61

Which of the following techniques can a project manager use to assist with quality planning? (Select Three).

- A. Peer review
- B. Critical Chain Method (CCM)
- C. Inspection
- D. Performance Evaluation and Review Technique (PERT)
- E. Work Breakdown Structure (WBS)

F. Benchmarking

Correct Answer: ACF

Section: (none)

Explanation

Explanation/Reference:

QUESTION 62

All of the following are part of the monitoring and controlling process group EXCEPT:

- A. updating the project charter.
- B. updating the project management plan.
- C. implementing change requests.
- D. updating the project scope.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 63

After identifying the activities in a work package, which of the following is the NEXT step that a project manager should complete?

- A. Estimate costs
- B. Identify activities
- C. Build a project schedule
- D. Assign key stakeholders

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 64

In which of the following organization types would a project manager have the LEAST amount of project authority?

- A. Functional
- B. Strong Matrix
- C. Balanced Matrix
- D. Weak Matrix

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 65

A project manager was asked to complete a project three weeks early and not crash the project. Which of the following should be done?

- A. Move some of the task to another release.
- B. Have the team work over time and give them time off later to save the budget.
- C. Continue to work and complete the project as soon as possible.
- D. Review the plan with the team and develop a way to reduce the time

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 66

The work breakdown structure (WBS) dictionary contains which of the following elements? (Select Three).

- A. Identification of stakeholders
- B. Description of work processes and procedures
- C. Quality control processes
- D. Estimated calendar time of activities
- E. Required resources
- F. Risk response strategies

Correct Answer: BDE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 67

One of the team members assigned to a project is not performing well. The team member is new and is not experienced in the type of work involved with this project. Which of the following is the BEST response to this situation?

- A. Ask other team members to help.
- B. Assign the team member to another project.
- C. Talk to the team member to encourage better performance.
- D. Arrange for training for the team member.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 68

A stakeholder has determined the need to update their payroll method with a new system. Which of the following is the FIRST activity the corporation should perform?

- A. Conduct a feasibility study.

- B. Determine the justification of the project.
- C. Obtain a preliminary review by the project selection committee.
- D. Determine if the project is in alignment with the company's strategic plan.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 69

A project manager is performing activity duration estimation. This project will have conditional decisions. Which of the following tools would be the BEST to use?

- A. GERT
- B. Gantt chart
- C. PERT
- D. EVM

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 70

A project manager is reviewing the ownership, date, and the necessary training for a deliverable. Which of the following documents would include this information?

- A. Transition plan
- B. Quality plan
- C. Change Control plan
- D. Procurement plan

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 71

Which of the following tools would be used to determine the relationship between two changed variables?

- A. Scatter diagram
- B. Qualitative risk analysis
- C. Ishikawa diagram
- D. Monte Carlo analysis

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 72

Which of the following is included in the project charter?

- A. A work performance report
- B. A cost assessment
- C. A high level plan
- D. A risk assessment

Correct Answer: C


Section: (none)

Explanation

Explanation/Reference:

QUESTION 73

Refer to the attached Exhibit.

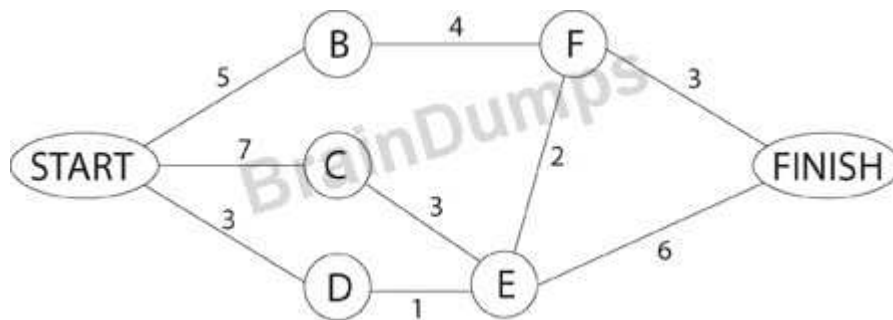

Which of the following is the float of path Start-C-E-Finish in the network diagram?

- A. Zero
- B. One
- C. Three
- D. Five

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 74

After final acceptance, which of the following would the project manager use to assess the strengths and weaknesses of the project?

- A. Post-project review
- B. Transition plan
- C. Project kick-off meeting
- D. Quality analysis

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 75

Which of the following is used to display a project schedule?

- A. Gantt chart
- B. Work Breakdown Structure (WBS)
- C. Pareto chart
- D. Ishikawa diagram

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 76

The project manager crashes a project that is behind schedule and under-budget. Which of the following will be the intended result?

- A. The project will be behind schedule and over-budget.
- B. The project will be on schedule but over-budget.
- C. The project will be on schedule and on-budget.
- D. The project will be behind schedule and on-budget.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 77

Several managers are sharing a project team member, which is impacting the progress of both projects. Which of the following BEST describes the situation?

- A. Varying work styles
- B. Schedule variance
- C. Scope creep
- D. Competing resource demands

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 78

A project manager is reviewing the ownership, date, and the necessary training for a deliverable. Which of the

following documents would include this information?

- A. Transition plan
- B. Quality plan
- C. Change Control plan
- D. Procurement plan

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 79

Which of the following shows a project that is presently over its financial budget?

- A. $CPI = 1.4$
- B. $CPI = 0$
- C. $CV = +\$11,000$
- D. $CPI = 0.8$

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 80

A major change has been approved by the change control board and it now needs to be scheduled for implementation. Which of the following is the BEST method of implementing the change?

- A. Distribute details of the change per the communication plan, and implement according to the change control process.
- B. Ask the change control board to schedule the change, and when scheduled, identify the individual team member responsible for implementing it.
- C. Email the project team, identifying the team member responsible for implementing the change, and then schedule it with the appropriate team members.
- D. Identify the team member responsible for implementing the change and direct the team member to inform the rest of the project team of the date and time of implementation.

Correct Answer: A


Section: (none)

Explanation

Explanation/Reference:

QUESTION 81

Refer to the attached Exhibit.

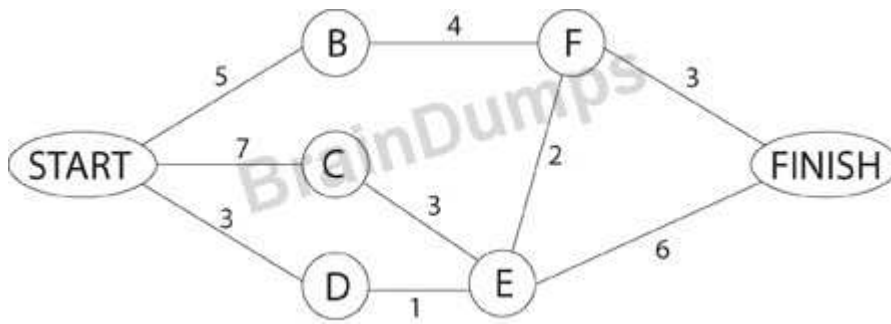

Which of the following is the float of path Start-C-E-Finish in the network diagram?

- A. Zero
- B. One
- C. Three
- D. Five

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 82

Which of the following is the purpose of a Pareto diagram?

- A. To show the sequence in which work will be performed
- B. To create the process that will complete the project
- C. To determine the critical path
- D. To direct team efforts to the areas that will have the most impact

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 83

Two members of a team have had difficulty working together in the past. Which of the following should the project manager do to facilitate communication between the team members?

- A. Discuss the problem at the next project meeting and have the team members find a solution.
- B. Evaluate both members and replace the least important member.
- C. Speak with both team members and address concerns.
- D. Dismiss both team members and replace them with new members.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 84

Which of the following is included in the project scope document? (Select Two).

- A. Quality metrics
- B. Work packages
- C. Assumptions
- D. Constraints
- E. Resource requirements

Correct Answer: CD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 85

Which of the following is a benefit of the work breakdown structure (WBS)?

- A. It will provide a detailed budget for the stakeholders.
- B. Items not included in the project objectives can be added to the WBS for flexibility.
- C. It will ensure that scope creep will not occur.
- D. Contains all activities required to complete the project.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 86

Transition plans include which of the following elements?

- A. Work Breakdown Structure (WBS)
- B. Project warranty
- C. Project process reports
- D. Earned value calculations

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 87

Which of the following occurs during a project kick-off meeting?

- A. Project plan approval
- B. Analyze project risks
- C. Identification of the stakeholders
- D. Project charter review

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 88

A project manager is conducting a root cause analysis with the project team. Which of the following tools should be utilized?

- A. Gantt chart
- B. Ishikawa diagram
- C. Network diagram
- D. Run chart

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 89

The project has been terminated. Which of the following should be conducted with the project team before they are released?

- A. Case study
- B. Feasibility analysis
- C. Stakeholder analysis
- D. Post-mortem analysis

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 90

A project manager conducted a risk probability and impact assessment with the project team. In which of the following risk management processes did this occur?

- A. Qualitative risk analysis
- B. Quantitative risk analysis
- C. Risk response planning
- D. Risk identification

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 91

Which of the following contract types places the LEAST amount of risk on the seller?

- A. Fixed-Price
- B. Cost-Plus-Fixed-Fee (CPFF)
- C. Cost-Plus-Fee (CPF)
- D. Time and material

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 92

A SPI of 1.1 means that the project is:

- A. under-budget.
- B. behind schedule.
- C. ahead of schedule.
- D. over-budget.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 93

A project manager should formally close out a project when:

- A. key project team members are needed to work on other projects.
- B. a key stakeholder is satisfied with the project deliverables.
- C. the CPI is 1.5 at the midpoint of the project.
- D. the project has been terminated unexpectedly.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 94

During the planning phase of the project, a subject matter expert (SME) estimates that one of the tasks identified for the project will take 120 hours to complete. Which of the following actions should the project manager take to make sure the work is scheduled correctly?

- A. Advise the SME that the work must be completed in less than 120 hours.
- B. Consult with others on the team to determine their estimates for the work.
- C. Further decompose the work of the task to no more than 80 hours.
- D. Increase the estimate to ensure work is completed on time.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 95

Which of the following BEST describes the definition of a project?

- A. Work undertaken to deliver a unique product or service
- B. Major work initiatives requested by an Executive Sponsor
- C. A yearly list of strategic goals for a company
- D. Work that can be decomposed to the task level

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 96

To ensure that project status meetings are effective and productive, the project manager should:

- A. invite only team members who have an immediate task on the project.
- B. publish an agenda prior to the meeting.
- C. invite all stakeholders and the sponsor to every meeting.
- D. hold only one meeting per week.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 97

Given the following information: Pessimistic estimate is 30 days Most Likely estimate is 15 days Optimistic estimate is 10 days Which of the following is the expected duration for this scheduled activity?

- A. 11 days
- B. 17 days
- C. 25 days
- D. 29 days

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 98

Which of the following defines a project? (Select Two).

- A. Limited time span

- B. Contains more than one deliverable
- C. Delivers a unique product or service
- D. Changes an ongoing process
- E. Generates positive returns

Correct Answer: AC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 99

Final project acceptance criteria are contained in which of the following?

- A. Transition plan
- B. Project scope document
- C. Project charter
- D. Quality plan

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 100

Which of the following sequences represents the correct order for implementing a change request?

- A. Change is requested, change impact analyzed, change request submitted to board, change request approved, change implemented.
- B. Change is requested, change implemented, change impact analyzed, change request submitted to board, change request approved.
- C. Change is requested, change request submitted to board, change impact analyzed, change request approved, change implemented.
- D. Change is requested, change request submitted to board, change request approved, change implemented, change impact analyzed.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

Exam B

QUESTION 1

Project information is received by the project manager in a number of different formats from team members. Which of the following would be the BEST way for the project manager to standardize the information?

- A. Create project templates.
- B. Require supervisor approval of documentation.
- C. Use document version control.
- D. Implement organizational format standards.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 2

Paperwork related to the project is not being signed in the correct order. The BEST way to correct this problem would be to implement a procedure for managing:

- A. required forms.
- B. document routing.
- C. change.
- D. document version control.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 3

Which of the following activities are associated with a project kick-off meeting? (Select Two).

- A. Obtaining a signature on the project charter.
- B. Communicating project goals and objectives.
- C. Communicating work package assignments.
- D. Creating a rough draft of the transition plan.
- E. Communicating stakeholder expectations.

Correct Answer: BE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 4

In regards to proper change management procedures, which of the following would be the FINAL activity?

- A. Coordinate with the appropriate stakeholders to determine course of action.
- B. Document the change using the appropriate change control forms.

- C. Perform impact analysis with project team members.
- D. Update the project plan components based on the approved change request.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 5

A company manager has turned in project objectives, and requests that the project manager start the project immediately. The project manager informs the company manager that the project cannot be started. Which of the following is an appropriate reason for not starting the project?

- A. Project sponsor approval has not been received.
- B. Projects can only be implemented by upper management.
- C. The project manager already has several ongoing projects.
- D. The project team has not been formed.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 6

Project team members are confused about their roles on a project. Which of the following is the FIRST technique the project manager can use to define their roles?

- A. Create a resource assignment matrix.
- B. Ask team members to define their roles.
- C. Have project sponsor assign their roles.
- D. Conduct stakeholder meeting to determine expectations.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 7

Which of the following is the purpose of a post-project review?

- A. Analyzes project performance
- B. Forms the control structure for the project
- C. Manages stakeholder expectations
- D. Identifies end products and intermediate deliverables

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 8

The project manager has outsourced a call center to a company in another region. The project manager receives reports that customers sometimes cannot hear the instructions given by call center employees. Which of the following is the MOST likely cause of the reports?

- A. Functional barriers
- B. Language barriers
- C. Technology barriers
- D. Communication preferences

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 9

Which of the following estimating types requires the MOST effort when creating a work breakdown structure (WBS)?

- A. Expert judgment
- B. Top-down
- C. Bottom-up
- D. Rough order of magnitude

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 10

A project has been delayed due to an ongoing labor dispute. The project sponsor asks the project manager to transfer the risk to complete the project on time. Which of the following is a method of transferring the risk?

- A. Delay the project
- B. Change the project schedule
- C. Outsource the project
- D. Hire more resources

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 11

Several team members have criticized the project manager for requesting that they work overtime in order to complete a project on time. Which of the following steps should the project manager take to resolve the conflict?

- A. Force the team members to work and terminate any who do not comply.
- B. Avoid the conflict by asking the stakeholders to talk to the team members.
- C. Compromise and let the team members finish the project late.
- D. Discuss schedule options with team members.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 12

Which of the following are common causes of project team conflict? (Select Two).

- A. Project schedule
- B. Competing resource demands
- C. Project budget
- D. Varying work styles
- E. Time zone differences

Correct Answer: BD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 13

Which of the following would be included in a project scope document? (Select Three).

- A. Project constraints
- B. Gantt chart
- C. Work Breakdown Structure (WBS)
- D. Project roles and responsibilities
- E. Key Performance Indicators (KPIs)
- F. Detailed project objectives

Correct Answer: AEF

Section: (none)

Explanation

Explanation/Reference:

QUESTION 14

A project change is approved by the Change Control Board that modifies the project scope. Which of the following is the NEXT step that the project manager should take?

- A. Construct a detailed plan to implement the change.
- B. Analyze the impact of the change request.
- C. Document the request in the change control log.
- D. Request a meeting with the project sponsor to discuss scope creep.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 15

Which of the following activities occur during a project kick-off meeting? (Select Three).

- A. Review of the risk management plan
- B. Review of the roles and responsibilities
- C. Review of the work breakdown structure (WBS)
- D. Review of the change management procedures
- E. Review of the project goals and objectives
- F. Review of the stakeholder expectations

Correct Answer: BEF

Section: (none)

Explanation

Explanation/Reference:

QUESTION 16

Which of the following personnel should sign the project charter?

- A. A representative from the project management office
- B. The project manager
- C. The most senior project team member
- D. An executive with the power to authorize the project

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 17

An ongoing project that is currently on schedule has had the required completion date moved up by one week; however, the project scope remains the same. Which of the following would be the effect on the project?

- A. Cost will decrease and time will increase.
- B. Cost will decrease and time will decrease.
- C. Cost will increase and time will increase.
- D. Cost will increase and time will decrease.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 18

Which of the following activity sequencing methods describes the start-to-start dependency?

- A. The completion of the successor activity depends upon the beginning of the predecessor activity.
- B. The completion of the successor activity depends upon the completion of the predecessor activity.
- C. The beginning of the successor activity depends upon the completion of the predecessor activity.
- D. The beginning of the successor activity depends upon the beginning of the predecessor activity.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 19

A project manager is performing activity duration estimation for a project. Using expert judgment the project manager has three values for each activity: the worst case, most likely case, and best case. Which of the following tools would be the BEST to use?

- A. Gantt chart
- B. PERT
- C. EVM
- D. GERT

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 20

A project manager is performing activity sequencing with the project team. Each activity is written in a box with arrows linking the boxes according to their dependencies. Which of the following tools is the project manager utilizing?

- A. Arrow Diagramming Method (ADM)
- B. Precedence Diagramming Method (PDM)
- C. Critical Path Method (CPM)
- D. Critical Chain Method (CCM)

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 21

A project manager is analyzing the network schedule to determine the early start and early finish dates as well as the late start and late finish dates, for each activity. The project manager is not taking into account any resource constraints. Which of the following methods is demonstrated in this scenario?

- A. Critical Chain Method (CCM)

- B. Precedence Diagramming Method (PDM)
- C. Arrow Diagramming Method (ADM)
- D. Critical Path Method (CPM)

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 22

A stakeholder wants information on how frequently the project manager will provide a status report. Which of the following documents would be the BEST place to find this information?

- A. Stakeholder analysis report
- B. Quality plan
- C. Work Breakdown Structure (WBS)
- D. Communication plan

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 23

The project sponsor has just requested a status report be emailed to all project stakeholders every two weeks. Which of the following documents needs to be updated?

- A. Communications plan
- B. Quality plan
- C. Stakeholder analysis report
- D. Work Breakdown Structure (WBS)

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 24

A project manager is performing activity sequencing. The project manager is only using start to finish dependencies. Dummy activities are being utilized to define all logical relationships. Which of the following methods is the project manager demonstrating?

- A. Precedence Diagramming Method (PDM)
- B. Critical Chain Method (CCM)
- C. Arrow Diagramming Method (ADM)
- D. Critical Path Method (CPM)

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 25

The project manager has been informed that the project team cannot procure any more materials until a new purchase order has been received. The project manager should record this information in which of the following documents?

- A. Risk response plan
- B. Communications plan
- C. Issues log
- D. Change control log

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 26

A project manager needs to identify uncertain events during the planning phase. Which of the following documents would be the BEST source of this information?

- A. Quality log
- B. Risk register
- C. Issues log
- D. Responsibility assignment matrix

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 27

Which of the following activities would happen FIRST in procurement management?

- A. Request seller responses.
- B. Perform a make or buy analysis.
- C. Perform contract administration.
- D. Perform vendor selection.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 28

Control limits would be found in which of the following plans?

- A. Procurement management plan
- B. Quality management plan
- C. Change management plan
- D. Scope management plan

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 29

The project manager needs to determine the relationship between two variables. Which of the following tools will the project manager use?

- A. Histogram
- B. Run chart
- C. Pareto chart
- D. Scatter diagram

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 30

The project cost performance index is 1.2 and the project manager has spent \$71,248 dollars to date. The project is currently 50 percent complete. Which of the following is the earned value (EV)?

- A. \$35,624.00
- B. \$59,373.33
- C. \$71,248.00
- D. \$85,497.60

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 31

A project manager is new to an organization and is about to begin work on a \$1,000,000 project. Which of the following would BEST help the project manager?

- A. Reviewing closure reports from previous projects within the organization.
- B. Asking stakeholders what standards they consider important.
- C. Developing a quality management plan.
- D. Talking to other project managers who have been with the organization for a long time.

Correct Answer: A

Section: (none)

Explanation**Explanation/Reference:****QUESTION 32**

A key stakeholder on a project advises the project manager that there is a component of the project that has yet to be decided. They are concerned that their needs regarding this component will not be addressed. In which of the following documents should the project manager record this information?

- A. Lessons learned
- B. Issue log
- C. Statement of Work (SOW)
- D. Project charter

Correct Answer: B

Section: (none)

Explanation**Explanation/Reference:****QUESTION 33**

A project manager is managing a project that is scheduled to take ten months to complete. The project is in its sixth month and \$450,000 has been spent. The project budget is \$990,000. Which of the following will the project manager use to determine the budgeted cost of work scheduled?

- A. Estimate to completion
- B. Planned value
- C. Cost performance index
- D. Budget at completion

Correct Answer: B

Section: (none)

Explanation**Explanation/Reference:****QUESTION 34**

The amount of time ahead or behind schedule on a project is called the:

- A. schedule baseline.
- B. schedule performance index.
- C. estimate to complete.
- D. schedule variance.

Correct Answer: D

Section: (none)

Explanation**Explanation/Reference:****QUESTION 35**

A project sponsor is adamant that a complex project must be completed within 12 months. Based on lessons

learned from previous projects of this type, the project manager believes that the project cannot possibly finish in less than 24 months. Which of the following tools can the project manager use to show the improbability of the proposed timeline?

- A. Pareto Diagram
- B. Decision tree
- C. Monte Carlo analysis
- D. Quantitative risk analysis

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 36

A network diagram shows two critical paths for a project. Which of the following will MOST likely increase?

- A. Staff
- B. Risk
- C. Cost
- D. Time

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 37

A project manager is responsible for meeting with the companys project review board to periodically evaluate the progress on a project. Which of the following is the role of the board?

- A. To supply audit trail oversight
- B. To ensure local standards compliance
- C. To provide decision oversight
- D. To communicate to stakeholders

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 38

Which of the following are components of an internal / external communication plan? (Select Two).

- A. Technology requirements
- B. Communication budget
- C. Distribution list
- D. Stakeholders list
- E. Communication frequency

Correct Answer: CE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 39

A project manager creates a detailed list of costs for each activity involved in the project and then uses the sum of the individual activities to create the budget. Which of the following cost estimating techniques was used?

- A. Bottom-up
- B. Expert judgment
- C. Parametric
- D. Top-down

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 40

Communication preferences, cultural differences, and language barriers are BEST described as which of the following?

- A. Special communication needs of project members
- B. Critical aspects of managing stakeholder expectations
- C. Items within the risk management plan
- D. Reasons for premature project failure / abandonment

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 41

A healthcare company must store project records for seven years. This is an example of which of the following?

- A. Document retention compliance
- B. ISO compliance
- C. Version control compliance
- D. Document version control

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 42

Post-mortem analysis occurs in which of the following process groups?

- A. Closing
- B. Pre-project setup
- C. Monitoring / controlling
- D. Planning

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 43

In pre-project setup, which of the following must be completed prior to validating a project?

- A. Project definition
- B. Preliminary SOW
- C. Project charter
- D. Stakeholder approval

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 44

Which of the following is the FINAL step in pre-project setup?

- A. Complete the work breakdown structure (WBS).
- B. Sign the approval document.
- C. Create the needed stakeholder forms.
- D. Validate the project.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 45

A key stakeholder has asked the project manager to complete the project a week earlier than expected. To accomplish this objective, the project manager will have to ask the project team to work overtime, which will increase the cost of the project. Which of the following should be the NEXT step?

- A. Ask the key stakeholder for more funding for the project.
- B. Ask the project team to work overtime to finish the project.
- C. Obtain an approved change control document before changing the project schedule.
- D. Agree to complete the project using the new schedule.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 46

There are three teams assigned to the same project. Two of the project teams are ahead of schedule; however, the product does not meet the needed quality standards. The third project team is behind schedule, but their product meets the quality standards. Which of the following should be the NEXT step for the project manager?

- A. Inform the stakeholders that the project is behind schedule.
- B. Meet with the teams to clarify the schedule and the quality standards expected.
- C. Crash the schedule to meet the project timeline.
- D. Fast track the schedule to complete the project on time without impacting the quality of the product.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 47

A new project manager has been assigned to a high profile project. In order to determine project status, which of the following should the project manager do? (Select Two).

- A. Ask the key stakeholders for the project status.
- B. Leave a voicemail message to key personnel requesting the project status.
- C. Schedule a meeting with the team members to determine the project status.
- D. Send an email to the team members to request project status reports.
- E. Schedule a meeting with the project sponsor to determine the project status.

Correct Answer: CD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 48

The project sponsor indicates that one of the key stakeholders is very unhappy with the project schedule. The other stakeholders are happy with the schedule. Which of the following is the MOST likely reason why the stakeholder is unhappy with the schedule?

- A. The stakeholder has unrealistic expectations.
- B. The project manager did not obtain buy-in from the stakeholder.
- C. The project manager did not discuss the schedule with the stakeholders.
- D. The project manager did not schedule the project team appropriately.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 49

A project manager has to complete an asset inventory project for a large corporation. Several departments have refused to allow access to the equipment to complete the project. The project manager should update which of the following?

- A. Change control form
- B. Risk register
- C. Work Breakdown Structure (WBS)
- D. Issues log

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 50

Two team members have been assigned to a specific project task. Neither can agree on how the task should be completed. Which of the following is the MOST likely cause of the problem?

- A. The project manager provided an unrealistic schedule.
- B. The team members have a personality conflict.
- C. The work package was not clearly defined.
- D. The team members have different management styles.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 51

Changing the project schedule to prevent a known risk is an example of which of the following risk responses?

- A. Mitigation
- B. Avoidance
- C. Acceptance
- D. Transference

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 52

Which of the following would be the MOST important objective of a kick-off meeting? (Select Two).

- A. To educate team members on what will be expected
- B. To give official notification for the project
- C. To inform the project sponsor on what will be expected

- D. To create a work breakdown structure (WBS)
- E. To develop the statement of work (SOW)

Correct Answer: AB

Section: (none)

Explanation

Explanation/Reference:

QUESTION 53

Which of the following is the BEST way to manage stakeholder expectations?

- A. Provide the stakeholder with a copy of the project charter.
- B. Approve stakeholder requests.
- C. Obtain stakeholder buy-in.
- D. Have the stakeholders complete a change request form.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 54

Three of the team members are having a conflict with each other. Which of the following steps should the project manager take to minimize the conflict?

- A. Resolve the conflict by terminating the team members.
- B. Ignore the conflict and keep working on the project.
- C. Encourage the team members to resolve the conflict.
- D. Ask the project sponsor to resolve the conflict.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 55

A key team member is performing poorly on a project. The project manager has verified that the team member knows the project expectations. The project manager has met repeatedly with this team member to outline expectations. Which of the following is the NEXT step the project manager should take to keep the project on schedule?

- A. Ignore the team members behavior.
- B. Terminate the team member.
- C. Move the team member to another project.
- D. Request the resource managers assistance.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 56

Which of the following is the BEST way for an organization to obtain qualified vendors?

- A. Use the largest vendors with access to enhanced resources.
- B. Use the vendors with the closest location for easy access.
- C. Use the established vendor approval process.
- D. Use the lowest priced vendors.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 57

In order to complete the pre-project setup, which of the following is the MOST important task of the project sponsor?

- A. Obtain funding for the project.
- B. Provide quality review of the deliverables.
- C. Provide leadership to the project team.
- D. Obtain resolution of the application development issues.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 58

Which of the following would require that the project risk register be updated?

- A. A qualitative risk analysis is performed
- B. A stakeholder has concerns about material delays
- C. The risk management plan is created
- D. Increased costs for required materials

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 59

A project manager is working with a large team on an important project. Many of the team members work remotely. The project manager requires each team member to submit weekly status reports at a certain time each week. One team member consistently submits late status reports. Which of the following should the project manager consider FIRST?

- A. Time zones for various work locations
- B. Necessity of weekly status reports
- C. Format of the status report
- D. Past performance reviews of the team member

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 60

A stakeholder asks the project manager to finish a project early. The project manager should ask the stakeholder to FIRST:

- A. speak to the other stakeholders to get their opinion.
- B. complete a change request form.
- C. speak to the project sponsor.
- D. consider how this might impact the quality of the product.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 61

A project sponsor is adamant that a complex project must be completed within 12 months. Based on lessons learned from previous projects of this type, the project manager believes that the project cannot possibly finish in less than 24 months. Which of the following tools can the project manager use to show the improbability of the proposed timeline?

- A. Pareto Diagram
- B. Decision tree
- C. Monte Carlo analysis
- D. Quantitative risk analysis

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 62

A Pareto chart is a special type of:

- A. histogram.
- B. Ishikawa diagram.
- C. scatter diagram.
- D. run chart.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 63

Which of the following is true of a work breakdown structure (WBS)? (Select Two).

- A. It consists of work packages at the top level which are decomposed to increasingly detailed levels.
- B. It is a quantitative analysis tool used in quality management to analyze defects.
- C. Each descending level represents an increasing detailed definition of the project work.
- D. It is developed during the planning process and used to create the project scope statement.
- E. It organizes and defines the total scope of the project.

Correct Answer: CE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 64

Which of the following is a benefit of a work breakdown structure (WBS)?

- A. It can determine the amount of progress on the project.
- B. It can quickly identify the projects major deliverables and underlying activities with graphical representation.
- C. It can quickly identify the probability and impact of project risks.
- D. It allows a real time analysis of actual project costs compared to the project baseline to determine the project variances.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 65

Which of the following describes a work breakdown structure (WBS) dictionary?

- A. A high level requirements document used to create the WBS.
- B. An alphabetical listing of WBS components detailing their associated project schedule dependencies.
- C. An organizational reference defining how WBS levels must be decomposed.
- D. A supporting document that provides more detail for the WBS components.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 66

Which of the following would require that the project risk register be updated?

- A. A qualitative risk analysis is performed
- B. A stakeholder has concerns about material delays
- C. The risk management plan is created
- D. Increased costs for required materials

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 67

The change control board has just approved a request to modify the sampling technique for a project. Which of the following documents would the project manager update?

- A. Risk management plan
- B. Quality management plan
- C. Communication management plan
- D. Scope management plan

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 68

A project manager is comparing their budgeting techniques to the most successful project in the company's history. Which of the following techniques is being utilized?

- A. Benchmarking
- B. Return on investment
- C. Process analysis
- D. Cost-benefit analysis

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 69

A project manager has determined the probability and impact of identified project risks. A meeting with the project team will be held to determine how to mitigate risks above the project threshold. Which of the following will be created during this meeting?

- A. Risk response strategies
- B. Risk register
- C. Risk assessment
- D. Stakeholder risk tolerance

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 70

A project manager can create a risk breakdown structure (RBS) to determine which of the following?

- A. Risk tolerance
- B. Risk probability
- C. Risk category
- D. Risk impact

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 71

The project is behind schedule. A project team member has analyzed the work performance information and has not created the weekly status update because they are uncertain when the update should be completed. Which of the following documents should the team member consult?

- A. Communication plan
- B. Risk plan
- C. Scope plan
- D. Quality plan

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 72

The change control board approved a request for \$25,000 to address rising labor costs of specialized trades. Which of the following documents should be updated?

- A. Scope statement
- B. Project schedule
- C. Resource requirements
- D. Project budget

Correct Answer: D

Section: (none)


Explanation

Explanation/Reference:

QUESTION 73

Refer to the attached Exhibit.

Task	Length (Days)
A	7
B	4
C	5
D	12
E	2
F	4

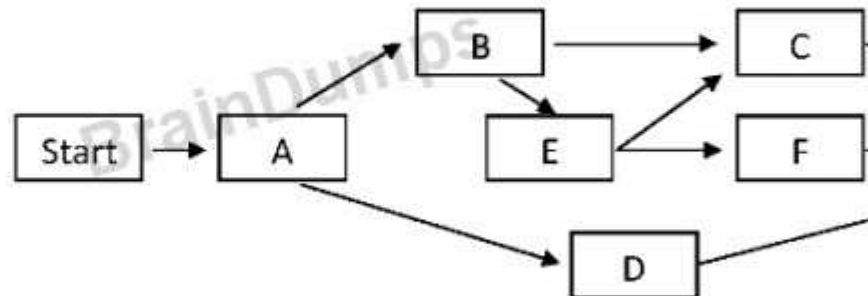

Which of the following is the duration of the critical path in the diagram?

- A. 2
- B. 5
- C. 6
- D. 7

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 74

The frequency of measurement would be found in which of the following documents?

- A. Risk management plan
- B. Scope management plan
- C. Quality management plan
- D. Communication management plan

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 75

The project has been terminated prematurely by the organization. Which of the following will the project manager need to complete?

- A. Case study

- B. Cost benefit analysis
- C. Quality assessment
- D. Post-mortem

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 76

A project manager has finished the first phase of a project. Who of the following determines if the project continues?

- A. End users
- B. Project manager
- C. Project team
- D. Project sponsor

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 77

The project has an AC of \$5,000. Which of the following would be used to determine the budget needed to complete the project?

- A. ETC
- B. PV
- C. BAC
- D. EAC

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 78

Which of the following skills would be the MOST useful in assembling an effective project team in a functional organization?

- A. Compromising
- B. Negotiation
- C. Estimating
- D. Padding

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 79

A project manager has been assigned two team members who do not get along. On past projects they have proven very difficult to work with and are often at odds with one another. Which of the following conflict resolution techniques would be BEST to address this?

- A. Forcing
- B. Avoiding
- C. Confronting
- D. Compromising

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 80

A project manager is receiving many requests for changes to a project. Which of the following did the project manager fail to complete?

- A. Proper project team selection
- B. Subject Matter Expert (SME) solicitation
- C. Milestone scheduling
- D. Stakeholder analysis

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 81

A project manager added some experienced team members to work on certain project activities in conjunction with inexperienced team members because the project is behind schedule. Which of the following BEST describes the technique the project manager is using?

- A. Schedule optimization
- B. Fast tracking
- C. Resource management
- D. Crashing

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 82

A team member reports that a system component they are working on causes the system to continually reboot.

The project manager should record this in which of the following documents?

- A. Quality management plan
- B. Communication plan
- C. Risk matrix
- D. Issue log

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 83

A project manager is working with a large team on an important project. Many of the team members work remotely. The project manager requires each team member to submit weekly status reports at a certain time each week. One team member consistently submits late status reports. Which of the following should the project manager consider FIRST?

- A. Time zones for various work locations
- B. Necessity of weekly status reports
- C. Format of the status report
- D. Past performance reviews of the team member

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 84

An experienced team member comes to the project manager to report that they are uncertain of the project requirements. This can MOST likely be attributed to:

- A. a poorly decomposed WBS.
- B. inadequate schedule analysis.
- C. inadequate resource management.
- D. improper risk planning.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 85

To determine the MOST likely estimate for the length of project activities, a project manager would use which of the following?

- A. PERT
- B. Gantt chart
- C. WBS Dictionary

D. SPI

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 86

A project manager receives a request for a minor change to one of the deliverables. Which of the following documents would MOST likely be impacted?

- A. Work Breakdown Structure (WBS)
- B. Project charter
- C. Communication plan
- D. Quality plan

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 87

In working with the risk management plan all of the following are ways of dealing with opportunities EXCEPT:

- A. exploiting.
- B. mitigating.
- C. sharing.
- D. enhancing.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 88

A project manager sits down to discuss with team members the strengths and weaknesses of a project. This is BEST described as:

- A. managing stakeholder expectations.
- B. post-project review.
- C. work performance review.
- D. human resource management.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 89

A project is approved in a series of stages. This is an example of:

- A. standards compliance.
- B. project version approval.
- C. stakeholder approval.
- D. phase gate approval.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 90

The purpose of the WBS is to:

- A. maintain standards compliance.
- B. manage change requests.
- C. determine work packages.
- D. aid in version control.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 91

Which of the following is a component of the cost management plan?

- A. Team member compensation
- B. Statement of Work (SOW)
- C. Project needs assessment
- D. Control limits

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 92

The project kick-off meeting is held:

- A. at the end of the planning process.
- B. before getting a signed project charter.
- C. during the initiating process.
- D. after the post review meeting.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 93

Which of the following is the BEST reason to conduct a feasibility analysis?

- A. To ensure that risks are addressed during the project
- B. To authorize a project
- C. To gather technical data
- D. To assign team member roles

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 94

A project manager has noted that a vendor is providing a poor quality product. The vendor states that its products meet the quality standards outlined in the current contract. Which of the following documents outline the contractual requirements?

- A. The statement of work (SOW)
- B. The milestone schedule
- C. The request for proposal (RFP)
- D. The work breakdown structure (WBS)

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 95

Two employees do not want to work with each other. The project manager tells the employees to perform the tasks or find other employment. Which of the following conflict resolution styles is being used?

- A. Forcing
- B. Withdrawing
- C. Compromising
- D. Accepting

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 96

Two employees will not work on the same project together. The project manager tells the employees to talk to their supervisors because the supervisors recommended they work together. This is an example of which of the

following conflict resolution styles?

- A. Withdrawing
- B. Forcing
- C. Accepting
- D. Compromising

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 97

The greatest amount of conflict occurs in which of the following team development stages?

- A. Storming
- B. Performing
- C. Norming
- D. Forming

Correct Answer: A

Section: (none)


Explanation

Explanation/Reference:

QUESTION 98

Refer to the attached Exhibit.

Task	Length (Days)
A	7
B	4
C	5
D	12
E	2
F	4

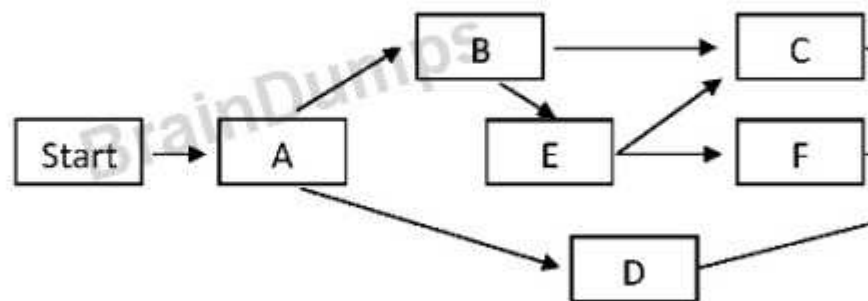

Which of the following dependencies is demonstrated between task 1 and task 2 in the following diagram?

- A. Start-to-Start

- B. Start-to-Finish
- C. Finish-to-Finish
- D. Finish-to-Start

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 99

Which of the following conflict resolution techniques is described as having one of the conflicting parties not deal with the problem?

- A. Negotiating
- B. Compromise
- C. Smoothing
- D. Avoiding

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 100

Although there is a difference of opinion among several team members, the project managers authority is used to keep the project moving forward. Which of the following conflict resolution techniques is being used by the project manager?

- A. Forcing
- B. Avoiding
- C. Negotiating
- D. Confronting

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

Exam C

QUESTION 1

Which of the following is the MOST common relationship used, when constructing a project schedule network diagram?

- A. Start-to-Finish
- B. Finish-to-Start
- C. Start-to-Start
- D. Finish-to-Finish

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 2

Which of the following may require a modification to the project scope baseline?

- A. An approved project change request
- B. A team member removed from the project
- C. A task that is falling behind schedule
- D. An identified product quality issue

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 3

In order to meet governmental requirement Q555, all materials must meet spec #A-223 qualifications. This is an example of which of the following types of dependencies? (Select Two).

- A. Internal
- B. Discretionary
- C. Fixed
- D. External
- E. Mandatory

Correct Answer: DE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 4

Which of the following is MOST likely to be included in a communication plan?

- A. Change request
- B. Risk register

- C. Frequency
- D. Statement of Work (SOW)

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 5

A project team is estimating the amount of time needed to perform an activity. They have recommended an optimistic, pessimistic, and most likely duration to complete the activity. Which of the following would be the BEST tool to estimate the final duration?

- A. PERT
- B. GANTT
- C. GERT
- D. WBS

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 6

Which of the following is a component of a project charter?

- A. Responsibility assignment matrix
- B. Risk register
- C. Work Breakdown Structure (WBS)
- D. Problem statement

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 7

Which of the following would MOST likely be reviewed during a project kick-off meeting?

- A. Change requests
- B. Work Breakdown Structure (WBS)
- C. Risk register
- D. Responsibility assignment matrix

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 8

Which of the following tools is the BEST to measure data organized in time sequence?

- A. Run chart
- B. Ishikawa diagram
- C. Pareto chart
- D. Histogram

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 9

Which of the following tools is the BEST to determine the cause of a problem?

- A. Run chart
- B. Pareto chart
- C. Ishikawa diagram
- D. Histogram

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 10

Which of the following documents would MOST likely be updated to reflect an approved time change for a regularly scheduled weekly status meeting?

- A. Work Breakdown Structure (WBS)
- B. Responsibility assignment matrix
- C. Communication plan
- D. Change request

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 11

During the execution phase of a project, a change request has been approved to add activities to the critical path without altering the schedule. Which of the following techniques will the project manager MOST likely use to deliver the project on time?

- A. Bottom-up estimating
- B. Rolling wave planning

- C. Resource leveling
- D. Fast tracking

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:



<http://www.gratisexam.com/>

QUESTION 12

A customer is reporting that the projects deliverables are not meeting the acceptance criteria. Which of the following documents MOST likely needs to be updated?

- A. Deliverable summary
- B. Quality checklist
- C. Risk register
- D. Resource assignment matrix

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 13

During the execution of an assigned task the developer informs the project manager of a missing component. Which of the following should the project manager do next?

- A. Inform the sponsor and have the developer include it in the same task.
- B. Document the change and determine the impact of the modification.
- C. Add the task to the project plan and assign the task to the developer.
- D. Inform the sponsor that the change is out of scope.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 14

Two SMEs disagree with the designed plan for a particular component. The project will be delayed if the plan is not approved today. The project manager demands the SMEs work together to incorporate their modifications by the close of business today. Which of the following resolution techniques was used?

- A. Negotiating
- B. Forcing

- C. Smoothing
- D. Compromise

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 15

The project is running behind schedule because one of the developers has taken an unscheduled vacation. The project manager informs the developer that any further unauthorized absence will result in removal from the project. Which of the following resolution techniques was used?

- A. Forcing
- B. Negotiating
- C. Avoiding
- D. Confronting

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 16

A project manager has been informed that a project deliverable must be completed by September 1st. Which of the following BEST describes this situation?

- A. Project assumption
- B. Project constraint
- C. Project risk
- D. Acceptance criteria

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 17

Which of the following is the BEST point for a project manager to join a project?

- A. Project initiation
- B. Project pre-planning
- C. Project planning
- D. Project executing

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 18

Which of the following are examples of a good business case for a new project? (Select Two).

- A. Increased profit opportunity for the customer
- B. Increased billing through maintenance contract
- C. Increased efficiency internally for the customer
- D. Increased engagement length with the customer
- E. Increased billing opportunity for the project team

Correct Answer: AC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 19

A project team has increased from six to twelve resources. How many total communication paths exist after the addition of resources?

- A. 24
- B. 48
- C. 66
- D. 144

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 20

In which of the following situations would a risk be placed in the upper right quadrant of a risk matrix?

- A. The team identified a risk to have a medium probability of occurrence and a high impact on project success.
- B. The team identified a risk to have a high probability of occurrence and a high impact on project success.
- C. The team identified a risk to have a low probability of occurrence and a high impact on project success.
- D. The team identified a risk to have a high probability of occurrence and a medium impact on project success.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 21

At a project milestone meeting, the project sponsor asked about a deliverable that is not on the project plan. Which of the following should the project manager do to compensate for this unmet expectation?

- A. Review the scope with the vendor.

- B. Review the scope with the customer.
- C. Review the scope with the team.
- D. Review the scope with the sponsor.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 22

The project scope document should outline which of the following project items? (Select Two).

- A. Services
- B. Lessons learned
- C. Products
- D. Schedule baselines
- E. Resource availability

Correct Answer: AC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 23

Which of the following is an input to a work breakdown structure (WBS)?

- A. Performance reports
- B. Stakeholder analysis
- C. Project scope statement
- D. Variance analysis

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 24

Which of the following should be included in a Gantt chart to analyze a project schedule? (Select Three).

- A. Risks
- B. Probability
- C. Cost analysis
- D. Start date
- E. Activity durations
- F. Finish date

Correct Answer: DEF

Section: (none)

Explanation

Explanation/Reference:

QUESTION 25

Which of the following can a project manager use to determine the critical path of a project? (Select Three).

- A. Business requirements
- B. Sequence of activities
- C. Completion date
- D. Stakeholder expectations
- E. Start date
- F. Risk register

Correct Answer: BCE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 26

Which of the following will have the GREATEST impact upon the outcome of a project? (Select Two).

- A. Quality metrics
- B. Scope creep
- C. Performance reports
- D. Project life cycle
- E. Project delays

Correct Answer: BE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 27

A stakeholder asks the project manager to finish a project early. The project manager should ask the stakeholder to FIRST:

- A. speak to the other stakeholders to get their opinion.
- B. complete a change request form.
- C. speak to the project sponsor.
- D. consider how this might impact the quality of the product.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 28

The communication plan for a project is a subset of which of the following documents?

- A. Project charter
- B. Risk management plan
- C. Project schedule
- D. Project plan

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 29

Whose approval should be obtained before modifying the scope of a project?

- A. Project team
- B. Executive management team
- C. Change control board
- D. Stakeholders

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 30

Which of the following are schedule compression techniques? (Select Two).

- A. Fast tracking
- B. Critical Path Method (CPM)
- C. Crashing
- D. PERT analysis
- E. Schedule network analysis

Correct Answer: AC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 31

Which of the following is the primary purpose of a project tollgate?

- A. Review the tasks from the next phase of the project.
- B. Review changes to a project.
- C. Get acceptance to move the project to the next phase of work.
- D. Give a status update on a set of deliverables.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 32

A project manager learns that a team member has falsified work experience, and does not have the knowledge required to complete the task. Which of the following should the project manager do?

- A. Reassign the individual to another role on the project team.
- B. Ignore the situation hoping that everything works out for the best.
- C. Assign other individuals to assist on the task to ensure the task does not get delayed further.
- D. Replace the member and ask the team manager to assign a more qualified person.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 33

Which of the following is a tool that can be used to identify project team members that are responsible for a task or deliverable?

- A. Project charter
- B. Work Breakdown Structure (WBS)
- C. Project schedule
- D. RACI chart

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 34

All of the following are taken into account when determining the critical path EXCEPT:

- A. Late start and finish dates.
- B. Activity durations.
- C. Early start and finish dates.
- D. Resource limitations.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 35

CORRECT TEXT

Which of the following techniques could a project manager use to determine a project schedule based upon a

variety of simulations?

- A.
- B.
- C.
- D.

Correct Answer:

Section: (none)

Explanation

Explanation/Reference:

Answer: Schedule network analysis

Answer: Critical chain method

Answer: Critical path method

Answer: Monte Carlo analysis

Answer: D

QUESTION 36

Which of the following steps should a project manager take to ensure the quality of project deliverables for a customer? (Select Two).

- A. The project manager should consult the project sponsor and customer to review the current quality requirements.
- B. The project manager should request a peer review of the project to determine if it meets the customers quality standards.
- C. The project manager should change the scope of the project to meet the customers expectations of quality standards.
- D. The project manager should check the finished product to determine if it meets the customers quality standards.
- E. The project manager should outsource to obtain the best resources for the project.

Correct Answer: BD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 37

During which of the following process groups is the availability of required resources for the project determined?

- A. Executing
- B. Monitoring/Controlling
- C. Initiating
- D. Planning

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 38

A project manager was asked to complete a project three weeks early and not crash the project.

Which of the following should be done?

- A. Move some of the task to another release.
- B. Have the team work over time and give them time off later to save the budget.
- C. Continue to work and complete the project as soon as possible.
- D. Review the plan with the team and develop a way to reduce the time

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 39

Which of the following would require that the project risk register be updated?

- A. A qualitative risk analysis is performed
- B. A stakeholder has concerns about material delays
- C. The risk management plan is created
- D. Increased costs for required materials

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 40

A project sponsor has requested that the training be delivered in parallel to a project's implementation in order to ensure the project is delivered on schedule. If accepted, this request is an example of:

- A. the critical path method.
- B. crashing.
- C. fast-tracking.
- D. rolling wave planning.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 41

Which of the following documents would be generated to solicit bids from outside vendors?

- A. WBS
- B. PERT
- C. RFP
- D. SOW

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 42

Which of the following conclusions can be drawn when a project has a CPI of 1.2?

- A. The project is taking longer than the estimated schedule.
- B. The project is costing less than the estimated budget.
- C. The project is taking less time than the estimated schedule.
- D. The project is costing more than the estimated budget.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 43

Which of the following represents the EAC of an ongoing project with an AC of \$100,000, a CV of \$10,000 and an ETC of \$50,000?

- A. \$90,000
- B. \$140,000
- C. \$150,000
- D. \$160,000
- E. The project is taking longer than the estimated schedule.
- F. The project is costing less than the estimated budget.
- G. The project is taking less time than the estimated schedule.
- H. The project is costing more than the estimated budget.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 44

Which of the following resource leveling techniques describes schedule compression by performing activities concurrently?

- A. Exploiting
- B. Crashing
- C. Optimizing
- D. Fast tracking

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 45

Which of the following describes a quality control tool used to analyze defects based upon number of occurrences?

- A. Pareto diagram
- B. Scatter diagram
- C. Fishbone diagram
- D. Ishikawa diagram

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 46

Which of the following is an important aspect of formal project closure?

- A. Assign resources to the next project.
- B. Analyze quality and ensure standards are being met.
- C. Document lessons learned for use in future projects.
- D. Modify the WBS to include all the change requests that occurred during the project.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 47

Which of the following would be the BEST tool to estimate activity time durations?

- A. Gantt chart
- B. CPM
- C. Estimating model
- D. PERT

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 48

Who has the MOST control over project scope changes?

- A. Key stakeholders
- B. Project sponsor
- C. Project manager
- D. Change control board

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 49

Monitoring and controlling project work is a control process function that spans from:

- A. the creation of the project work plan to the completion of the work breakdown structure (WBS).
- B. project kickoff to the project completion, including documentation of lessons learned.
- C. project kickoff to the project plan generation.
- D. the creation of the project work plan to the completion of the statement of work (SOW)

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 50

A project has been cancelled during the execution phase. Which of the following steps should be taken?

- A. Continue to work the project.
- B. Finish the project charter and project plan.
- C. Complete lessons learned document.
- D. Develop the project transition plan.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 51

A project manager seeks to implement a change control system. Which of the following elements are essential for this system to be effective? (Select Three).

- A. Change request form
- B. Sponsor communication
- C. Approval mechanism
- D. Pareto chart
- E. Impact analysis
- F. Earned Value (EV) analysis

Correct Answer: ACE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 52

In order to prepare a project charter, which of the following items are required for the pre-project setup?

- A. Assumptions, constraints, project deliverables, and all resources required for the project.
- B. Client name, client project manager, organization project manager, and a complete project budget.
- C. Direction from team members, development methodology, and staff requirements.
- D. Business need, assumptions, constraints, project deliverables, and staff requirements.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 53

In order to validate a project, which of the following is required to complete a stakeholder analysis?

- A. Verify the project stakeholders needs, wants, and expectations are turned into requirements.
- B. Verify the project stakeholders have been selected by the project manager to provide the best scope for the project.
- C. Verify the project team members will be able to provide the expected stakeholder results.
- D. Verify the project stakeholders needs are documented in the work breakdown structure (WBS).

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 54

Which of the following is the purpose of a milestone schedule?

- A. A detailed summary of the project milestones that need to be achieved.
- B. A summary level timetable of the major project milestones.
- C. A summary of the anticipated milestones and the issues identified for the project.
- D. A detailed summary of the anticipated milestones and risks identified for the project.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 55

Which of the following are characteristics of an approved project charter? (Select Two).

- A. Provides the prioritization of work from the stakeholders.
- B. Defines the project managers authority.
- C. Identifies what the project manager wants to derive from the project.
- D. Increases the number of just-in-time processes required to decrease scope creep.
- E. Validates the existence of a project.

Correct Answer: BE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 56

Which of the following is the main objective for a work breakdown structure (WBS)?

- A. To develop a proven methodology that will assist the project manager with the delegation of authority.
- B. To decompose the project down into manageable parts.
- C. To develop the estimating and detailed scheme of the project.
- D. To build on individual development, independent of the team efforts.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 57

Which of the following is the correct formula for computing a projects SPI?

- A. $SPI = EV - AC$
- B. $SPI = EV / PV$
- C. $SPI = EV - PV$
- D. $SPI = EV / AC$

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 58

An ongoing project has a BAC of \$450,000, an EV of \$110,000 and an AC of \$100,000.

Which of the following is the CPI of the project?

- A. \$340,000
- B. 1.1
- C. \$10,000
- D. .91

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 59

In a highway project 5 miles (8 kilometers) out of the total 15 miles (24 kilometers) have been completed. The

BAC is \$900,000. Which of the following represents the EV of this project?

- A. \$150,000
- B. \$300,000
- C. \$450,000
- D. \$600,000

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 60

In a highway project 5 miles (8 kilometers) out of the total 15 miles (24 kilometers) have been completed. The BAC is \$900,000. Which of the following represents the ETC of this project?

- A. \$150,000
- B. \$300,000
- C. \$450,000
- D. \$600,000

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 61

Which of the following are characteristics of a projects critical path? (Select Two).

- A. The critical path is the longest duration.
- B. The critical path has the least amount of resources.
- C. The critical path is the shortest duration.
- D. The critical path has less than or equal to zero float time.
- E. The critical path has a greater than zero float time.

Correct Answer: AD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 62

A project sponsor has requested that weekly status updates are to be sent by email, detailing the schedule performance index (SPI) and schedule variance (SV) of the project. In which of the following documents should these requirements be included?

- A. Communications management plan
- B. Cost management plan
- C. Project charter
- D. Contract management plan

Correct Answer: A
Section: (none)
Explanation

Explanation/Reference:

QUESTION 63

Which of the following processes incorporates the make-or-buy analysis?

- A. Procurement management
- B. Risk management
- C. Quality management
- D. Scope management

Correct Answer: A
Section: (none)
Explanation

Explanation/Reference:

QUESTION 64

The method of cost-estimating whereby the costs of the individual work packages are aggregated to form the full cost-estimate is called:

- A. parametric estimating.
- B. bottom-up estimating.
- C. expert judgment.
- D. analogous estimating.

Correct Answer: B
Section: (none)
Explanation

Explanation/Reference:

QUESTION 65

A project has a CPI of 0.6. Which of the following would BEST describe the cost-efficiency of the project?

- A. The costs are currently over the estimates.
- B. The costs and the estimates are about the same.
- C. The costs are currently under the estimates.
- D. The earned value is greater than the actual cost.

Correct Answer: A
Section: (none)
Explanation

Explanation/Reference:

QUESTION 66

The EV of a particular project is \$6 million. The CV is -\$340,000. Which of the following can be determined

from this information?

- A. The project costs are currently under-budget.
- B. The AC is less than the EV.
- C. The EV is higher than the AC.
- D. The project costs are currently over-budget.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 67

Cause and effect diagrams are also referred to as:

- A. run charts.
- B. Pareto charts.
- C. histograms.
- D. fishbone diagrams.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 68

In order to compare a current projects quality to that of a previously completed project, a project manager should use which of the following techniques?

- A. Process improvement
- B. Quality metrics
- C. Benchmarking
- D. Cost-benefit analysis

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 69

A quality control technician is diagramming test results on a run chart. The chart consists of twenty-five points, with twelve consecutive points below the median line; however, the other thirteen points alternate above and below the median line. The twelve consecutive points represent which of the following?

- A. The run denotes common cause variation.
- B. The quality process is flawed and should be completed again.
- C. The product does not adhere to specification.
- D. The run denotes special cause variation.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 70

A stakeholder has indicated that a three phase project must be completed in four months instead of the previously agreed upon six months. It is determined that fast-tracking the project is the only option. Which of the following is a characteristic of fast-tracking a project?

- A. Minimizes risk due to decreased timeline.
- B. Requires planning and execution to be completed in parallel.
- C. Minimizes cost since work is completed in four months instead of six.
- D. Requires rework due to decreased timeline.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 71

A new critical requirement has been identified after the project charter was approved. Which of the following is the NEXT step the project manager should take?

- A. Convene another meeting with the entire group reviewing the requirements one last time and incorporating the additional requirement.
- B. Determine the effort of the missing requirement and incorporate it into the work plan.
- C. Revise the approved requirements document and forward to the project team for review.
- D. Generate a change request and submit it to the change control board for review.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 72

Two team members refuse to work together and have undermined the project with their constant bickering. The project manager needs both of them to complete the project. The team members meet and agree to work at different times. Which of the following conflict resolution styles is being used?

- A. Forcing
- B. Smoothing
- C. Confronting
- D. Compromising

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 73

If the EV is \$3,000 and the AC is \$4,000, which of the following would be the CPI for the project?

- A. .50
- B. .75
- C. 1.25
- D. 1.75

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 74

Which of the following would be the impact upon a project if the CPI for the project is .75?

- A. The project is under-budget.
- B. There would be a 25 percent cost decrease.
- C. There would be a 75 percent cost increase.
- D. The project is over-budget.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 75

If the EV is \$3,000 and the AC is \$4,000, which of the following is the CV for the project?

- A. -\$1,000
- B. \$1,000
- C. -\$3,000
- D. \$3,000
- E. There would be a 25 percent cost decrease.
- F. There would be a 75 percent cost increase.
- G. The project is over-budget.
- H. The project is under-budget.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 76

Which of the following are the benefits of a work breakdown structure (WBS)? (Select Two).

- A. It determines the project milestones.

- B. It determines the project budget.
- C. It outlines the communication plan for the team.
- D. It determines the resources required to complete project tasks.
- E. It outlines the statement of work (SOW) for the project.

Correct Answer: BD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 77

When a project ends unexpectedly, which of the following should the project manager do?

- A. Create an end document to add to the file before moving on to another project.
- B. Create a document identifying the negative impact of the early project ending to give to the customers management.
- C. Perform project close out with full documentation and review.
- D. Perform a limited project close that consists of releasing team members.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 78

It is important to complete a formal project closure process to: (Select Three).

- A. assure that the customer will work with all vendors in the future.
- B. confirm that the stated project objectives were met.
- C. confirm that the customer accepts the final deliverables.
- D. collect new information to enter into the issue log for further review.
- E. assure that the contract is complete and the team members can be released.
- F. collect additional scope requirements that need to be entered into the project plan.

Correct Answer: BCE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 79

Which of the following would be the benefit of saving a project binder in a centralized location?

- A. Provides an opportunity for another project manager to review the binder and make corrections.
- B. Provides an opportunity for team members to review their contributions.
- C. Provides other project managers the opportunity to review the project information.
- D. Provides stakeholders the opportunity to modify the change request forms.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 80

When would a project manager have a closure meeting? (Select Three).

- A. Stage completion
- B. Task completion
- C. Document completion
- D. Project cancellation
- E. Project completion
- F. Vendor cancellation

Correct Answer: ADE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 81

Which of the following occurs during administrative closure?

- A. Requiring input from the sponsor on the project objectives.
- B. Updating quality expectations for the deliverables.
- C. Closing out contracts with vendors.
- D. Revealing new WBS tasks to team members.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 82

Faced with a complex project with many stages, which of the following is the BEST action for the project manager to take?

- A. Employ phase closure meetings.
- B. Encourage vendors to work overtime.
- C. Request a schedule extension.
- D. Hire additional contractors.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 83

A project manager wants to have complete control of the project team members. Which of the following organization structures would allow for this?

- A. Functional
- B. Balanced matrix
- C. Strong matrix
- D. Projectized

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 84

Which of the following would be contained in the problem statement within the project charter?

- A. The issues that might block a vendor's success.
- B. The conflict between management and the project vendors.
- C. The issues the customer wants resolved.
- D. The conflict management style that will be used during the project.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 85

Which of the following is the BEST definition of a stakeholder? (Select Two).

- A. Anyone impacted negatively by the project.
- B. Anyone who is in the company where the project is taking place.
- C. Anyone who is interested in the project.
- D. Anyone who negatively impacts the project.
- E. Anyone impacted positively by the project.

Correct Answer: AE

Section: (none)

Explanation

Explanation/Reference:

QUESTION 86

Before a change request is presented to the change control board, which of the following should the project manager do?

- A. Suggest the board study the cost of the change.
- B. Evaluate the affect on all other parts of the project.
- C. Review the change request with the project sponsor.
- D. Request team member input on the value of the change.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 87

Which of the following documents should be used to present the length of identified tasks?

- A. CPM
- B. Key event/activity list
- C. PERT
- D. Gantt

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 88

Which of the following can the project manager do to manage scope creep?

- A. Be open minded to new ideas to the project.
- B. Be flexible about what needs to be done to complete the project.
- C. Be specific when defining project objectives in the project plan.
- D. Be positive when approached with changes to ensure customer satisfaction.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 89

Which of the following should a project manager do to actively track issues as they are identified?

- A. Develop a quality management plan.
- B. Create a process for anonymous team review of issue resolution.
- C. Make an issues log template.
- D. Update the issues log.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 90

A project manager was called into the office of the Chief Information Officer (CIO) and informed that the resource budget for the company has been reduced by 10%. The CIO expects that the project must be completed on time.

Which of the following will be impacted?

- A. Project scope will be impacted.
- B. Quality will be impacted.
- C. WBS will be impacted.
- D. SOW will be impacted.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 91

Quality assurance is performed during which phase of a project?

- A. During the controlling phase
- B. During both controlling and execution phase
- C. During the execution phase
- D. During the planning phase

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 92

A project manager has decided to reduce the impact of a possible threat. Which of the following risk response strategies BEST describes this action?

- A. Avoidance
- B. Exploiting
- C. Mitigation
- D. Acceptance

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 93

During a status meeting, a team member informs the project manager of a possible risk. Which of the following is the FIRST action the project manager should take?

- A. Record the risk in the risk register.
- B. Work with the team to develop a risk response.
- C. Perform an initial prioritization of the risk.
- D. Determine the probability and impact of the risk.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 94

A project manager has just completed the planning of a project, but cannot start the project execution until granted permission from the project sponsor. This is an example of which of the following actions?

- A. Stakeholder analysis
- B. Risk assessment
- C. Audit review
- D. Phase gate

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 95

The project manager has documented a change request from a key project stakeholder. Which of the following actions should the project manager take NEXT?

- A. Discuss this change during the next status meeting.
- B. Ask other stakeholders for recommendations.
- C. Send the request to the change control board.
- D. Perform an impact analysis.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 96

The change control board has approved a change to the scope of a project. Which of the following actions should the project manager take NEXT?

- A. Obtain additional approval from the project sponsor.
- B. Discuss this change during the next status meeting.
- C. Perform a probability and impact analysis on the change.
- D. Create a plan to implement the change.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 97

A project manager has analyzed work performance information and identified alarming variances in the project deliverable. Which of the following would be the BEST response for the project manager?

- A. Perform a qualitative risk assessment.
- B. Speak with the project sponsor about possible solutions.
- C. Approve a change request to correct the actions.
- D. Recommend corrective actions.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 98

A project manager is completing a project schedule network diagram using dummy activities to show all logical relationships. Which of the following tools is the project manager using?

- A. ADM
- B. WBS
- C. AON
- D. PDM

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 99

A project manager needs to replace someone on the project team. Which of the following is the FIRST action they should take?

- A. Consult the project staffing plan.
- B. Notify the human resources department to open a job posting.
- C. Search for skilled subcontractors who could quickly fill the opening.
- D. Ask the project sponsor for another resource.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 100

Which of the following documents would a project manager review to determine all the identified risks on a project?

- A. Risk matrix
- B. Risk register
- C. Risk response
- D. Risk baseline

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

Exam D

QUESTION 1

The initial quality measurements used to determine if a variance has occurred is known as the:

- A. Quality checklist.
- B. Baseline.
- C. Quality metrics
- D. Control limit.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 2

Which of the following BEST describes the chart of accounts?

- A. The numbering system used to monitor the quality measurements during the life of the project.
- B. The numbering system used to track project costs depending on their activity type.
- C. The numbering system used to decompose project activities into sub-project activities.
- D. The numbering system used to identify each activity on the work breakdown structure.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 3

Which of the following would MOST likely contain warranty information for the project deliverable?

- A. Scope statement
- B. Cost baseline
- C. Risk assessment
- D. Transition plan

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 4

Before the execution phase begins, who is in control of the project?

- A. Project sponsor
- B. Program manager
- C. Project manager
- D. Project coordinator

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 5

An adjustment to the project has been approved and funding granted, but the project manager feels the modification is out of scope.

Which of the following should the project manager do?

- A. Schedule a meeting with the project sponsor to reject the adjustment.
- B. Refuse to make the adjustment and send a recommendation to the review board.
- C. Make the adjustment and wait for another review.
- D. Make the adjustment but document the concern.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 6

The project team has completed phase testing. After testing, a subject matter expert (SME) notices that a component was skipped.

Which of the following should the project manager do?

- A. Proceed with the release and document the adjustment in the change log.
- B. Proceed with the release and tell the SME the component will be added in a special release.
- C. Delay the release until the component is tested.
- D. Schedule a meeting with the stakeholders to review the impact.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 7

Who should conduct lessons learned when an outside vendor is used?

- A. The project coordinator because they are responsible for the project and vendor.
- B. The resource manager because they are responsible for the vendors actions.
- C. The program manger because they control the project budget.
- D. The project manager because they are responsible for the entire project.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 8

A project manager is using a vendor with a fixed bid contract. The vendor would like to help out with other parts of the project.

Which of the following should the project manager do NEXT?

- A. Review the vendors SOW and determine if the additional work items can be included.
- B. Allow the vendor to accept the additional work on a time and material (T&M) basis.
- C. Allow the vendor to accept the additional work, but honor the fixed bid price.
- D. Explain to the vendor that the work is already assigned to the vendor with the lowest cost.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 9

Which of the following is the BEST reason to review the historical information from a similar project?

- A. To get a good idea of the writing style of the project manager.
- B. To get an understanding of the number of managers within the organization.
- C. To get an understanding of the resources needed to complete the project.
- D. To get an understanding of the document approval process.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 10

A project manager must initially address a performance issue with a project team member.

Which of the following communication methods is BEST to use?

- A. Formal written communication
- B. Informal verbal communication
- C. Informal written communication
- D. Formal verbal communication

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 11

The initiation process concludes with the creation of which of the following?

- A. Contingency reserve
- B. Project charter

- C. Project schedule
- D. Project scope statement

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 12

A Pareto diagram focuses attention on which of the following?

- A. Identifying the stage of failure during the process
- B. Predicting future problems based on historic results
- C. Checking for variances in quality over time
- D. Locating defects with the highest occurrence

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 13

Which of the following is the BEST report to provide to senior management?

- A. Daily progress report
- B. Milestone report
- C. Quality audit
- D. Work performance report

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 14

Which of the following is an appropriate risk response for diverting a portion of the project risk?

- A. Avoiding
- B. Sharing
- C. Enhancing
- D. Exploiting

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 15

Who has the MOST control over project scope changes?

- A. Key stakeholders
- B. Project sponsor
- C. Project manager
- D. Change control board

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 16

Which of the following is created as part of the closing phase?

- A. Quality baseline
- B. Cost review
- C. Activity estimation
- D. Feasibility analysis

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 17

After a change control board meeting, which of the following actions should the project manager do NEXT?

- A. Notify the requester of the verdict.
- B. Review the impact of proposed change.
- C. Update the project scope statement.
- D. Document the specific change request.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 18

A project manager is implementing a new community park and wants to build public support. Which of the following communication mediums would BEST facilitate the goal?

- A. Send a personally signed letter to the residents.
- B. Hold a public ceremony at the location for the residents.
- C. Hold a teleconference for residents.
- D. Send an email to the community residents.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 19

A project manager notices that status meetings are poorly attended and that one or two team members try to dominate the meetings. Which of the following should the project manager do to make the project status meetings more productive? (Select Two).

- A. Include agenda items in the meeting invitation.
- B. Ensure that the meetings start and end on time.
- C. Provide criticism to poor team performers.
- D. Allow the team members to set the tone of the meeting.
- E. Discuss issues during the meeting until they are resolved.

Correct Answer: AB

Section: (none)

Explanation

Explanation/Reference:

QUESTION 20

A hurricane is forecasted near the corporations call center. The project manager has arranged for a redundant call center in another location to accept calls if the corporate call center is unable to receive calls. Which of the following risk responses is the project manager using?

- A. Avoidance
- B. Acceptance
- C. Mitigation
- D. Transference

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 21

Several project tasks cannot be completed because local resources are not available. The project manager has to outsource the work to find qualified resources. Which of the following risk responses is the project manager using?

- A. Acceptance
- B. Mitigation
- C. Transference
- D. Avoidance

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 22

By completing the lessons learned during project closure, the project manager can:

- A. modify the project budget.
- B. determine the reasons for the success or failure of a project.
- C. manage stakeholder expectations.
- D. determine the critical path of the project schedule.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 23

An important team member will not be available to complete a project. The project manager selects a new team member and trains the new team member on the project tasks. The project manager is using which of the following risk response techniques to resolve the issue?

- A. Monitor the risk
- B. Mitigation of the risk
- C. Acceptance of the risk
- D. Transference of the risk

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 24

Which of the following shows a project that is presently over its financial budget?

- A. $CPI = 1.4$
- B. $CPI = 0$
- C. $CV = +\$11,000$
- D. $CPI = 0.8$

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 25

Which of the following would a project manager do NEXT after selecting a vendor for a project?

- A. Determine a list of qualified sellers.
- B. Determine vendor resource availability.
- C. Hold a bidders conference.

D. Negotiate the contract.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 26

Which of the following shows the number of communication channels for a team with twelve stakeholders?

- A. 56
- B. 66
- C. 72
- D. 132
- E. Determine vendor resource availability.
- F. Hold a bidders conference.
- G. Negotiate the contract.
- H. a list of qualified sellers.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 27

The schedule estimates for a particular work package that is underway were not properly considered and the timescales are too tight. Which of the following methods should the project manager select to investigate?

- A. PDM
- B. SPI and SV
- C. CPM
- D. Issues log

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 28

A team member on a project uncovers a minor risk with the quality of a purchased component. The team uses their combined expert judgment to determine that the risk to the deliverable is very low. Which of the following is the MOST likely action the project manager should take?

- A. Issue a change request to the change control board to select a different vendor from the qualified sellers list and request early termination of the current vendors contract.
- B. Call a project team meeting to discuss the risk and communicate the issue directly with the project sponsor.
- C. Contact the vendor and request a thorough review of the products architecture.
- D. Document the risk in the risk register, accept it and refer to the agreed vendor contracts for methods of raising the issue with the vendor.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 29

The change control board has requested that a project manager evaluate the impact of a major change request that will affect the timetable of several work-packages. Which of the following actions should the project manager undertake FIRST?

- A. Create a modified version of the project schedule applying the critical path method.
- B. Call a project team meeting to use combined expert judgment to accept or reject the change request.
- C. Create a Pareto chart for the outputs from the specific work-packages identified by the change control board.
- D. Crash the schedule to meet the original deadlines.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 30

A project manager has been engaged to deliver a project in South America and does not speak Spanish. More than 50 percent of the project team will be Spanish speaking. Which of the following would be the project managers BEST option?

- A. Insist that all communication be in English.
- B. Use automated translation technologies to communicate with team members in writing.
- C. Engage only bi-lingual team members.
- D. Engage interpreters at both locations for all key team communication.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 31

Which of the following is the method for determining the critical path of a project?

- A. Determine the BAC of a project and the AC at completion; calculate the difference.
- B. Examine the project schedule and determine the two most critical milestones; then calculate the total time from the start of the first determined milestone to the end of the second.
- C. Examine the project schedule and place all scheduled activities on one time-line, regardless as to whether they are being implemented in parallel. Then calculate the total time taken.
- D. Examine the project schedule and calculate the total time taken for all scheduled activities, from commencement of the project to closure, with zero float.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 32

During handover stage a customer of a particular project noticed the extended warranty from a particular vendor for a critical application has not been ordered. In which of the following documents should this have been previously addressed?

- A. Procurement management plan
- B. Project charter
- C. Staffing management plan
- D. Risk management plan

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 33

A variance between the planned scheduled work and the actual work completed would initially be highlighted in which of the following performance statistics?

- A. CV
- B. SV
- C. CPI
- D. ETC

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 34

Which of the following is the correct progression of the project life cycle?

- A. Planning, initiating, executing, monitoring / controlling, closing
- B. Initiating, planning, executing, monitoring / controlling, closing
- C. Planning, initiating, monitoring / controlling, executing, closing
- D. Initiating, planning, monitoring / controlling, executing, closing

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 35

A project is cancelled unexpectedly prior to completion. Which of the following would the project manager use to document the details of the project closure?

- A. Histogram
- B. Post mortem
- C. SWOT analysis
- D. Project scope statement

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 36

Which of the following is a representation of the difference between the planned costs of work completed compared to the actual cost at a point in time?

- A. EV
- B. CPI
- C. CV
- D. AC

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 37

Which of the following is a representation of the amount of money spent on project work at a point in time?

- A. CV
- B. CPI
- C. EV
- D. AC

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 38

An ongoing project requires several parts manufactured at an outside vendor. If the vendor has sufficient quantity and can still ship today, the parts should be received in five days; although in most cases an order of this size requires ten days. Allowing for an upcoming holiday and some potential bad weather the shipment could take up to twenty-one days. Using the PERT method, which of the following is the correct time estimate for a parts delivery?

- A. 10 days
- B. 11 days
- C. 21 days
- D. 36 days

Correct Answer: B
Section: (none)
Explanation

Explanation/Reference:

QUESTION 39

Which of the following is a quantitative risk analysis tool or technique?

- A. Risk register
- B. Decision tree analysis
- C. Probability and impact matrix
- D. Cause and effect diagram

Correct Answer: B
Section: (none)
Explanation

Explanation/Reference:

QUESTION 40

Which of the following describes a qualitative risk analysis tool that assigns ratings to project risk factors based upon the likelihood of occurrence and the affect it will have on the project?

- A. Cause and effect diagram
- B. Risk register
- C. Probability and impact matrix
- D. Decision tree analysis

Correct Answer: C
Section: (none)
Explanation

Explanation/Reference:

QUESTION 41

Which of the following would be considered a valid strategy in response to an adverse risk?

- A. Exploit
- B. Monitor
- C. Mitigate
- D. Enhance

Correct Answer: C
Section: (none)
Explanation

Explanation/Reference:

QUESTION 42

A project team is comprised of team members based in North America, Europe, the Middle East and the Far

East. Which of the following is the MOST efficient means of reporting project updates to all team members?

- A. E-mail to all team members
- B. A daily web conference
- C. A weekly conference call
- D. Face to face meeting at a central location

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 43

All of the following should be detailed in the communications management plan EXCEPT:

- A. the person responsible for communicating the information.
- B. team member roles and responsibilities.
- C. team members that will receive the information.
- D. frequency of project team communications.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 44

Which of the following is a characteristic of a project charter?

- A. Issued by the project manager with support from the project sponsor.
- B. Links the project to the on-going work of the organization through a business plan.
- C. Formally recognizes the existence or establishment of the project.
- D. Provides low-level requirements for the project.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 45

Which of the following is included within the RFP?

- A. Identify the price quote and include the communication plan.
- B. Request a price and the names of the project resources.
- C. The vendor that will complete the work and the vendors background, history and experience.
- D. Request total cost for all work to be completed and procedures for replying to the bid.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 46

Work must be overlapped and completed in parallel rather than sequentially within the critical path in order to meet the end date of the project. Which of the following would be utilized?

- A. Optimizing
- B. Crashing
- C. Resource leveling
- D. Fast-tracking

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 47

Pareto charts helps the project manager with which of the following?

- A. Determine if a process will be experiencing difficulties.
- B. Focus on creative thinking.
- C. Explore required future events.
- D. Focus on the most critical issues to improve quality.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 48

Which of the following is used in quality control?

- A. Pareto chart
- B. RACI matrix
- C. PERT
- D. Issues log

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 49

To ensure the quality of implemented project change requests, which of the following will need to occur? (Select Two).

- A. The project team is not notified of the approved change.

- B. Change is tracked and is either accepted or rejected by the change control board.
- C. Change is logged and updated in the change log document.
- D. Once a change is forwarded to the change control board, it will be removed from the change log.
- E. Once the change is submitted to the change control board, it will be approved and placed into production.

Correct Answer: BC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 50

Several stakeholders and the project sponsor have indicated that they are not being supplied with project updates. As the project manager, which of the following should be done to address the situation?

- A. Create a communication roles template.
- B. Speak in-depth personally to each stakeholder.
- C. Send emails to everyone on the project team.
- D. Refer to the communications plan.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 51

During execution, a project manager of a construction project requires certain project team members to work outdoors, atop tall buildings. Which of the following would BEST mitigate the risk of injury to those team members, without affecting the approved project schedule?

- A. Ensure that project team members do not work in very windy weather.
- B. Ensure that project team members are furnished with slip-resistant boots.
- C. Ensure that project team members are trained in injury response.
- D. Ensure that project team members are covered by applicable insurance.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 52

A project manager decides to manage the threat of a particular risk through the purchase of an insurance policy. Which of the following risk response strategies is being applied?

- A. Avoidance
- B. Transfer
- C. Acceptance
- D. Mitigation

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 53

A qualitative analysis identified a server crash as an internal project risk with a medium probability and high adverse impact to the project. The project manager decides to manage this risk by authorizing the purchase and installation of a tape backup unit for the server, to prevent the potential loss of documents. Which of the following risk response strategies was applied in this circumstance?

- A. Acceptance
- B. Transfer
- C. Mitigation
- D. Avoidance

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 54

Which of the following is found in project closure documentation?

- A. Updated communications plan
- B. Quality baseline
- C. Responsibility assignment matrix
- D. Transition plan

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 55

A project manager receives a memo from a key stakeholder in the project. The memo states that going forward they should be notified of all scope changes, but not involved in the decision making process. Which of the following should the project manager do NEXT?

- A. Initiate a transition plan.
- B. Assign the stakeholder to the change control board.
- C. Schedule a meeting with the stakeholder.
- D. Update the communication plan.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 56

Which of the following is the BEST way for a project manager to conduct a lessons learned session?

- A. Talk about different conflict resolution techniques that could be used in the future.
- B. Talk about specific task failures and who is responsible for the failures.
- C. Talk about processes needing improvement versus things that went wrong.
- D. Talk about the project vendor shortcomings and contractual failures.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 57

A project manager has an initial problem with a remote team members performance. Which of the following is the BEST form of communication to address this issue?

- A. Formal written communications
- B. Informal written communications
- C. Informal verbal communications
- D. Formal verbal communications

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 58

The project manager has three stakeholders with whom they need to communicate (not including the project manager). There are six channels of communication. A new stakeholder has been added to the project that the project manager needs to communicate with. How many communication channels are now existent?

- A. 7
- B. 10
- C. 12
- D. 16

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 59

The formal process that must be performed at the end of the project to provide the final inspection of the product is called:

- A. methodology verification.
- B. scope verification.
- C. change verification.

D. system verification.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 60

A manager and the head of engineering discuss a change to a major work package. After the meeting, the project manager contacts a third person and tells them to complete the paperwork to make the change. Who did the project manager contact?

- A. A project sponsor
- B. A third party vendor
- C. A change control board member
- D. A project expeditor

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 61

A project manager is managing the delivery of a project awarded under a fixed-cost contract. The project cost was poorly planned and underestimated, but the projects overall scope and deadline cannot change. Failure to deliver the project is not an option. Which of the following will MOST likely be affected by these circumstances?

- A. Earned Value (EV)
- B. Quality
- C. Change management
- D. Resource leveling

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 62

Which of the following is created during the initiation phase?

- A. Project scope statement
- B. Statement of Work (SOW)
- C. Project charter
- D. Work Breakdown Structure (WBS)

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 63

Which of the following is the MOST common precedence dependency type?

- A. Start-to-Start
- B. Finish-to-Start
- C. Start-to-Finish
- D. Finish-to-Finish

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 64

Which of the following correctly identifies the application of a projects quality management plan?

- A. Quality assurance and quality control both occur in the monitoring / controlling phase.
- B. Quality control occurs in the execution phase, quality assurance occurs in the monitoring / controlling phase.
- C. Quality assurance occurs in the execution phase, quality control occurs in the monitoring / controlling phase.
- D. Quality assurance and quality control both occur in the execution phase.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 65

Which of the following is the effect of triple constraint on a project?

- A. A change in one constraint can be approved by the project sponsor.
- B. A change in one constraint may cause a change in another constraint.
- C. At least two constraints must change before there is an effect on the project.
- D. Changing all three constraints will cause the project to be closed.

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 66

A project manager is two weeks into a project when an unexpected delay occurs. Material that is needed to complete the project could be available in three business days; however, the project team believes that estimate is unrealistic and that it will take five business days for the material to arrive. The project manager was informed by another employee in the material company that it could take up to thirteen days to receive the materials. Which of the following estimates should be given to the project sponsor?

- A. 5 business days
- B. 6 business days

- C. 8 business days
- D. 13 business days

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 67

The project manager has the MOST authority in which of the following organizational structures?

- A. Balanced Matrix
- B. Functional
- C. Weak Matrix
- D. Strong Matrix

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 68

A project manager is in a projectized organization managing a particular project. A department manager has repeatedly requested a change to the scope of the project which was previously denied. The project is currently behind schedule. Which of the following would be the BEST way to deal with the managers repeated request?

- A. Request the manager fill out a formal request for the change and file it with the project management office.
- B. Have a team member meet with the manager so the project can stay on schedule.
- C. Ask the project sponsor to respond to the department manager.
- D. Implement the change as requested by the manager and inform the project sponsor.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 69

Which of the following describes the LOWEST level of a work breakdown structure (WBS)?

- A. Technical specifications
- B. Project performance reports
- C. Work packages
- D. Functional specifications

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 70

During final inspection, a project team member finds a deficiency in the product. In which of the following did this action occur?

- A. Gap analysis
- B. Quality control
- C. Process audit
- D. Quality assurance

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 71

A project manager has just completed the work breakdown structure (WBS) with the project team. Which of the following would be used during activity sequencing?

- A. Precedence diagramming method
- B. Monte Carlo analysis
- C. Resource availability
- D. Resource leveling technique

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 72

A project manager has received a change request. Which of the following is the NEXT step?

- A. Approve the change and notify the project sponsor that cost can be reduced.
- B. Re-baseline the project budget because this change will decrease the expenditures.
- C. Send the change to the project sponsor for approval.
- D. Analyze the change to determine the impact.

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 73

Which of the following is a reason why the project kick-off meeting is important?

- A. It will introduce the team to the projects goals and objectives.
- B. It will provide a detailed timeline for the project and its deliverables.
- C. It will make the executive sponsor aware of project expectations.

D. It will define the scope of the project.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 74

Crashing a schedule involves which of the following?

- A. Performing a re-baseline of the project schedule
- B. Performing critical path activities simultaneously
- C. Adding resources to critical path activities
- D. Estimating the earned value of the project activities

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 75

Which of the following is an example of risk mitigation?

- A. Reduce the likelihood of the risk.
- B. Transfer ownership of the risk.
- C. Update the risk management plan.
- D. Change the project scope to eliminate the risk.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 76

Which of the following describes a work breakdown structure (WBS)?

- A. Determines the critical path of a project schedule
- B. Identifies stakeholders and their roles
- C. Is deliverable-oriented and hierarchical in nature
- D. Measures the quality of the project objectives

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 77

During the execution phase, a customer approaches the project manager demanding a change. Which of the

following are the steps the project manager should take? (Select Two).

- A. Make the change.
- B. Notify the Executive Sponsor.
- C. Fill out a change request form.
- D. Evaluate the impact of the change.
- E. Deny the change.

Correct Answer: CD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 78

A project team member informs the project manager that they have added functionality to enhance the product. The team member did not inform the project manager prior to making the change. Which of the following should the project manager do in this situation?

- A. Remove the team member from the team and assign them to another project.
- B. Remove all enhancements to the product and proceed as was originally stated.
- C. Document the enhancement and send to the change control board.
- D. Advise the team member that they cannot request future changes.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 79

During execution of the project, the project sponsor informs the project manager that a requirement needs to be added to the scope statement. Which of the following is the FIRST action that the project manager should take?

- A. Evaluate the impact of the change on the project.
- B. Call the project team members together to determine how to handle the change.
- C. Change the work breakdown structure (WBS) to include all the tasks involved with this change.
- D. Rewrite the statement of work (SOW) to include the proposed change.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 80

Which of the following are reasons why formal project closure is important? (Select Three).

- A. Release staff from the project
- B. Reassign staff to another project
- C. Releases leftover funding from the project

- D. Provides historical information
- E. Allows for final changes to the work breakdown structure (WBS)
- F. Confirms completed/non-completed objectives

Correct Answer: ADF

Section: (none)

Explanation

Explanation/Reference:

QUESTION 81

When does stakeholder identification initially take place?

- A. When the organizational structure is determined
- B. Once the project charter document is created
- C. Once the project planning phase is entered
- D. When documenting the project objectives

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 82

Which of the following documents is used when assigning resources to scheduled tasks?

- A. Work Breakdown Structure (WBS) dictionary
- B. Cost management plan
- C. WBS
- D. Approved project charter

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 83

Various technologies exist to complete a project, but the project manager is not well versed in these technologies. Which of the following can the project manager initiate to assist with the decision?

- A. A Statement of Work (SOW)
- B. A project needs assessment
- C. A vendor contract
- D. A Request for Proposal (RFP)

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 84

Information regarding training, extended support, and warranties are detailed in the:

- A. Risk register
- B. Project scope statement
- C. Work breakdown structure (WBS)
- D. Transition plan

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 85

Several project team members are in conflict about the lighting in their office and the noise level. Which of the following describes this type of conflict?

- A. Forming
- B. Competing resource demands
- C. Varying work styles
- D. Expert judgment

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 86

A project manager is concerned that certain aspects of a project may not meet the local regulations. Which of the following is the project manager concerned with?

- A. Standards compliance
- B. Phase gate approval
- C. Internal process compliance
- D. Company compliance

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 87

In an attempt to make a deadline, a North American project manager is able to procure emergency funding for additional people. The resources are located in Europe. Which of the following project components will have to be updated to reflect working with a new time zone location?

- A. Communication plan
- B. Risk management plan

- C. Work Breakdown Structure (WBS)
- D. Project scope statement

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 88

When ensuring the quality of project deliverables, which of the following is the NEXT step the project manager should take, once performance information has been gathered?

- A. Create Gantt charts
- B. Generate change requests
- C. Identify variances
- D. Implement change requests

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 89

Which of the following is the FINAL step in the pre-project setup phase?

- A. Obtain signed approval of the project charter.
- B. Obtain signed approval of the statement of work (SOW).
- C. Conduct a feasibility analysis for the project.
- D. Create the work breakdown structure (WBS).

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 90

Which of the following is described when a company requires version control of project documents?

- A. Decision oversight
- B. Regulatory compliance
- C. Internal process compliance
- D. Change management controls

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 91

A new technology being implemented will result in project team member layoffs. Which of the following actions can the project manager take to address team member concerns?

- A. Cancel the project
- B. Host a meeting to provide a status update
- C. Outsource the project
- D. Select a different technology that will not result in layoffs

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

QUESTION 92

When are project closure procedures determined?

- A. During the planning phase
- B. During the monitoring/controlling phase
- C. During the closure phase
- D. During the execution phase

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 93

Which of the following would be included in a project scope document? (Select Two).

- A. Project constraints
- B. WBS dictionary
- C. Project assumptions
- D. Project charter
- E. Work Breakdown Structure (WBS)

Correct Answer: AC

Section: (none)

Explanation

Explanation/Reference:

QUESTION 94

Which of the following is the BEST tool to determine how the frequency of an individual cause contributes towards the total result?

- A. SWOT analysis
- B. Critical Chain Method (CCM)
- C. Ishikawa diagram

D. Pareto chart

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 95

During which of the following process groups is the project charter developed?

- A. Pre-project setup
- B. Project execution
- C. Project planning
- D. Project control

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 96

Which of the following steps should be taken to formally close a project? (Select Two).

- A. Finalize the project charter
- B. Create a statement of work (SOW)
- C. Verify client sign-off of the project deliverables
- D. Document the lessons learned
- E. Finalize the work breakdown structure (WBS)

Correct Answer: CD

Section: (none)

Explanation

Explanation/Reference:

QUESTION 97

A major change has been approved by the change control board and it now needs to be scheduled for implementation. Which of the following is the BEST method of implementing the change?

- A. Distribute details of the change per the communication plan, and implement according to the change control process.
- B. Ask the change control board to schedule the change, and when scheduled, identify the individual team member responsible for implementing it.
- C. Email the project team, identifying the team member responsible for implementing the change, and then schedule it with the appropriate team members.
- D. Identify the team member responsible for implementing the change and direct the team member to inform the rest of the project team of the date and time of implementation.

Correct Answer: A

Section: (none)

Explanation

Explanation/Reference:

QUESTION 98

Which of the following would a project manager organize and implement in order to provide decision oversight to scope changes?

- A. Request for Proposal (RFP)
- B. Quality management plan
- C. Change control board
- D. Version control system

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 99

Which of the following contract types places the LEAST amount of risk on the seller?

- A. Fixed-Price
- B. Cost-Plus-Fixed-Fee (CPFF)
- C. Cost-Plus-Fee (CPF)
- D. Time and material

Correct Answer: D

Section: (none)

Explanation

Explanation/Reference:

QUESTION 100

Control limits would be found in which of the following plans?

- A. Procurement management plan
- B. Quality management plan
- C. Change management plan
- D. Scope management plan

Correct Answer: B

Section: (none)

Explanation

Explanation/Reference:

Exam E

QUESTION 1

Three of the team members are having a conflict with each other. Which of the following steps should the project manager take to minimize the conflict?

- A. Resolve the conflict by terminating the team members.
- B. Ignore the conflict and keep working on the project.
- C. Encourage the team members to resolve the conflict.
- D. Ask the project sponsor to resolve the conflict.

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:

QUESTION 2

Several project tasks cannot be completed because local resources are not available. The project manager has to outsource the work to find qualified resources. Which of the following risk responses is the project manager using?

- A. Acceptance
- B. Mitigation
- C. Transference
- D. Avoidance

Correct Answer: C

Section: (none)

Explanation

Explanation/Reference:



<http://www.gratisexam.com/>
